

VISTARA PM PORTFOLIO

Retrospective Documentation of Real PM Work

Divya G D | Project Manager

divyagowdrudinesh@gmail.com | +91 9945607229

[linkedin.com/in/divya-g-d-824b5b367](https://www.linkedin.com/in/divya-g-d-824b5b367)

GitHub: <https://github.com/divyagowdrudinesh/vistara-pm-agent>

4 Epics · 42 Stories · 9 Sprints · ~150 Story Points

Vistara Animation & Cinematic Visual Effects (OPC) Pvt. Ltd, Davanagere | 2022–2026

Section 1: Executive Summary

This portfolio retrospectively documents real Project Management work delivered at Vistara Animation & Cinematic Visual Effects (OPC) Pvt Ltd between 2022–2026, recreated in Jira and Confluence using a custom Python agent built on the Jira REST API and Anthropic Claude API.

The Vistara Journey

A 5-year arc from informal proprietorship (2020) to formalized OPC Pvt. Ltd. structure (registered May 2024, CIN: U85500KA2024OPC188895), with a B.Sc. degree expansion vision that did not materialize due to enrolment shortfalls — leading to company shutdown in January 2026. The portfolio captures PM execution across four major workstreams: Animation programme launches in partnership with BIET, Brochure production, the annual Cinemotsava showcase event, and partner-college workshops paired with industry placement pipeline development.

Portfolio Scope

4 epics, 42 stories (+ 9 subtasks), 9 sprints, ~150 story points — with full acceptance criteria, sprint reports, velocity tracking, and supporting Confluence documentation including PRDs, project charters, strategic plans, and 1-1 meeting notes.

Two Things This Portfolio Proves

This isn't a fabricated project for the sake of a portfolio. Every story, milestone, and stakeholder reference reflects real work executed at a real institution. The framing demonstrates two things in parallel — (1) enterprise-grade PM rigor applied to startup-scale operations, and (2) AI-assisted technical fluency through a working Python agent that automated Jira workflow creation end-to-end.

⚠ A note on retrospective documentation: Because this work was logged in Jira in 2026 rather than during the original 2022–2026 execution window, some Jira-generated views (burndown charts, timeline, velocity for early sprints) appear stretched or batched. This is a deliberate trade-off — the goal is to document and demonstrate enterprise PM rigor on real work, not to fabricate live sprint data. Where Jira's native views distort, the underlying data — story counts, story points, acceptance criteria, sprint structure, completion rates — remains accurate and verifiable.

Section 2: Context — The Real Vistara Work

Vistara Animation & Cinematic Visual Effects was an animation and VFX training institute based in Davanagere, Karnataka, founded by Dinesh G K (Director) and Chethan Kumar (Head Faculty). The organization began as a sole proprietorship, scaled operationally through strategic infrastructure decisions and external partnerships, and formally registered as an OPC Pvt. Ltd. in May 2024 with a vision to launch B.Sc.-affiliated degree programmes in 2026.

That B.Sc. expansion did not materialize. Enrolment shortfalls in the target batch meant the institution could not sustain the degree programme model. Vistara shut down in January 2026. This portfolio documents the PM execution that happened in the years before that outcome — real delivery, real constraints, real stakeholder ecosystems.

Organizational Timeline

Period	Event
Jul 2020 – Jun 2022	Administrative Liaison — pre-OPC proprietorship phase
Jul 2022	PM role begins; OPC Pvt. Ltd. transition vision established
Feb 2023	RG Institute workshops delivered (3-day + 6-day)
May 2024	Vistara OPC Pvt. Ltd. formally registered (CIN: U85500KA2024OPC188895)
Jun–Jul 2024	BIET partnership MoU executed; operational base embedded at BIET campus
Sep 2024	8-programme go-to-market brochure delivered
Oct 2024	Snappy Lime partnership formalised (CEO: Manjunath Hegde)
Jan 2025	Sripada Studios placement partnership (CEO: P V Phani Srivatsa)
Feb 12, 2025	Cinemotsava 2025 executed at GMIT — 200+ participants
Jan 2026	Company shutdown — B.Sc. expansion did not materialize
Mar–Apr 2026	Retrospective Jira/Confluence portfolio built

The Operating Model

Vistara operated an asset-light model by design. The most significant infrastructure decision was the closure of the standalone MCC B-Block headquarters (Rs. 50,000/month lease) in favor of an embedded operational base at BIET at Rs. 5,000/month under a formal MoU — a 90% rent reduction without disrupting programme delivery. GMIT served as a workshops and events venue (including Cinemotsava 2025), with a B.Sc. launch arrangement that remained pending at company shutdown.

The BIET partnership was formalized via MoU on June 25, 2024, with operations commencing July 1, 2024. Vistara provided curriculum, faculty, and software; BIET provided campus lab infrastructure.

Stakeholder Ecosystem

Partner	Type	Relationship
GMIT	Academic	Workshops & events venue (Cinemotsava 2025); B.Sc. launch arrangement pending at shutdown
BIET	Academic	Operational base — MoU signed Jun 2024, Rs. 5K/month
RG Institute	Academic	Workshop delivery only
Sripada Studios	Industry	Placement pipeline — CEO: P V Phani Srivatsa
Snappy Lime	Industry	Hiring & distribution — CEO: Manjunath Hegde

Internal stakeholders: Dinesh G K (Director), Chethan Kumar (Head Faculty), Sunil (Faculty), Kiran Kumar C M and Imran Khan (Programme Managers, Cinemotsava 2025).

Section 3: Portfolio Architecture — 4 Epics

The portfolio is structured as four epics in Jira, each corresponding to a distinct PM workstream. The screenshot below shows all four epics on the VAI board.

VAI board

Q Search wo... Filter Group Saved filters

Work	Priority	Reporter	Assignee	Status	Resol
> VAI-4 Partner College Workshops & Industry Placem...	Medium	DD Divya G D	DD Divya G D	DONE	Done
> VAI-3 Cinemotsava 2025 — Annual Film & Gaming Ev...	High	DD Divya G D	DD Divya G D	DONE	Done
> VAI-2 Brochure Production — Programme Portfolio	High	DD Divya G D	DD Divya G D	DONE	Done
> VAI-1 Animation — Programme Launch	High	DD Divya G D	DD Divya G D	DONE	Done

+ Create 4 of 4

VAI board — all 4 epics: VAI-4 Partner Workshops, VAI-3 Cinemotsava, VAI-2 Brochure Production, VAI-1 Animation Programme Launch. All DONE.

Epic	Sprints	Stories / Points
Epic 1 — Animation Programme Launch (BIET x Vistara)	Sprints 1–3	10 stories / ~30 pts
Epic 2 — Brochure Production	Sprints 4–5	8 stories + 2 subtasks / ~24 pts
Epic 3 — Cinemotsava 2025	Sprints 6–7	14 stories + 4 subtasks / 32 pts
Epic 4 — Partner Workshops & Placement Pipeline	Sprints 8–9	10 stories + 3 subtasks / ~18 pts

Epic 1 — Animation Programme Launch (BIET x Vistara)

10 stories across Sprints 1–3. Covers the five execution gates for launching the BIET-affiliated Animation semester: curriculum confirmation against BIET BOS syllabus, faculty scheduling, Adobe/Autodesk license procurement, lab infrastructure readiness, and student enrolment. Sprint start June 2024 in anticipation of the BIET MoU, which formalized July 1, 2024.

Outcome: 100% sprint completion, zero P1 failures on Programme Day 1. Identified faculty dependency risks in sprint planning and escalated to the Director for contingency planning.

Search wo...  Filter Group					Saved filters   ...	
☐	Work	Priority	Reporter	Assignee		
☐	>  VAI-4 Partner College Workshops & Industry Placement Pipeline	Medium	 Divya G D	 Divya G D		
☐	>  VAI-3 Cinemotsava 2025 — Annual Film & Gaming Event	High	 Divya G D	 Divya G D		
☐	>  VAI-2 Brochure Production — Programme Portfolio	High	 Divya G D	 Divya G D		
☐	▼  VAI-1 Animation — Programme Launch	High	 Divya G D	 Divya G D		
☐	☒  VAI-14 Conduct post-semester NPS survey and retrospective	Low	 Divya G D	 Divya G D		
☐	☒  VAI-13 Publish Week 1 status report to Confluence	Medium	 Divya G D	 Divya G D		
☐	☒  VAI-12 Submit semester-end feedback forms and student satisfaction survey — Sem 6	Medium	 Divya G D	 Sunil		
☐	☒  VAI-11 Onboard enrolled students — ID, fee receipt, schedule issued	High	 Divya G D	 Divya G D		
☐	☒  VAI-10 Open student enrolment — documentation pack ready	High	 Divya G D	 Sunil		
☐	☒  VAI-9 Complete lab infrastructure readiness check	High	 Divya G D	 Chethan Kumar		
☐	☒  VAI-8 Procure Autodesk Maya licenses — all lab seats	High	 Divya G D	 Divya G D		
☐	☒  VAI-7 Procure Adobe Creative Cloud licenses — all lab seats	High	 Divya G D	 Divya G D		
☐	☒  VAI-6 Finalize faculty timetable — all modules covered	High	 Divya G D	 Divya G D		
☐	☒  VAI-5 Confirm BIET BOS curriculum for current semester	High	 Divya G D	 Divya G D		

Epic 1 expanded — VAI-5 through VAI-14: curriculum confirmation, faculty timetable, licensing, infrastructure, enrolment, and onboarding. All DONE. VAI-12 title updated to remove compliance reference not personally owned.

Epic 2 — Brochure Production

8 stories + 2 subtasks across Sprints 4–5. End-to-end production of the 8-programme go-to-market brochure — Vistara's first formal collateral following OPC registration. Work covered PRD authoring, design brief, vendor management, multi-round review cycles, Director sign-off, and multi-channel distribution across digital and print.

Outcome: Single-session Director approval, zero revision loops post-sign-off. Sprint 4 carries a documented lesson: two stories were transitioned to Done after sprint close, creating an 'Issues Not Completed' flag on the sprint report (see Section 7, Bug 6).

Q Search wo...

DD

CK

Filter

Group

Saved filters ...

☐	Work	Priority	Reporter	Assignee	
☐	> VAI-4 Partner College Workshops & Industry Placement Pipeline	Medium	DD Divya G D	DD Divya G D	
☐	> VAI-3 Cinemotsava 2025 — Annual Film & Gaming Event	High	DD Divya G D	DD Divya G D	
☐	▼ VAI-2 Brochure Production — Programme Portfolio	High	DD Divya G D	DD Divya G D	
☐	☒ VAI-22 Distribute brochure via Snappy Lime — digital and print channels activated	Medium	DD Divya G D	Unassigned	
☐	▼ ☒ VAI-21 Receive and archive final print-ready and digital PDF files from designer	Medium	DD Divya G D	Unassigned	
☐	VAI-24 Confirm print vendor has received print-ready PDF	Medium	DD Divya G D	Unassigned	
☐	☒ VAI-20 Director final approval — Dinesh G K sign-off on Draft 2	Medium	DD Divya G D	Unassigned	
☐	☒ VAI-19 Incorporate revision feedback — designer produces Draft 2	Medium	DD Divya G D	Unassigned	
☐	▼ ☒ VAI-18 Review Draft 1 — visual quality and layout sign-off by PM	Medium	DD Divya G D	Unassigned	
☐	VAI-23 Consolidate VAI-17 and VAI-18 feedback into single revision brief document	Medium	DD Divya G D	Unassigned	
☐	☒ VAI-17 Review Draft 1 — technical content accuracy sign-off by Chethan Kumar	Medium	DD Divya G D	Unassigned	
☐	☒ VAI-16 Draft design brief and brief external designer	Medium	DD Divya G D	Unassigned	
☐	☒ VAI-15 Extract curriculum content — all 8 programmes via 1-1 sessions with Chethan ...	Medium	DD Divya G D	Unassigned	
☐	▼ VAI-1 Animation — Programme Launch	High	DD Divya G D	DD Divya G D	

+ Create

4 of 4

+ Create

4 of 4 ↻

Epic 2 expanded — VAI-15 through VAI-22 covering content extraction, design brief, two review cycles (technical + visual), Director sign-off, file archival (with subtask VAI-24), and distribution.

Epic 3 — Cinemotsava 2025

14 stories + 4 subtasks across Sprints 6–7. Full event lifecycle for Cinemotsava 2025: collaboration agreement with Vishistaa Cine Journey, venue approval from GMIT, budget and competition structure, flier production (with Director sign-off subtask), event ground setup, and post-event conversion analysis.

Outcome: Delivered at GMIT on February 12, 2025. 200+ participants, zero on-day P1 incidents, positive qualitative feedback from GMIT faculty, the co-organiser (Vishistaa Cine Journey), and participating industry guests.

Search wo...	Filter	Group	Saved filters			
Work	Priority	Reporter	Assignee			
VAI-3 Cinemotsava 2025 — Annual Film & Gaming Event	High	DD Divya G D	DD Divya G D			
VAI-36 Post-event retrospective and next-event planning	Medium	DD Divya G D	Unassigned			
VAI-37 Post-event analysis — track admission conversions across 7 courses	Medium	DD Divya G D	Unassigned			
VAI-36 Execute Cinemotsava event day — Feb 12, 2025	Medium	DD Divya G D	Unassigned			
VAI-42 Coordinate guest of honour arrival, introduction, and hospitality	Medium	DD Divya G D	Unassigned			
VAI-41 Manage competition judging and winner selection	Medium	DD Divya G D	Unassigned			
VAI-35 Prepare event grounds and coordinate caterers — weekend setup	Medium	DD Divya G D	Unassigned			
VAI-34 Finalize prize amounts based on registration count	Medium	DD Divya G D	Unassigned			
VAI-33 Invite industry partners as guests of honour	Medium	DD Divya G D	Unassigned			
VAI-32 Invite GMIT lecturers and HoDs as event attendees	Medium	DD Divya G D	Unassigned			
VAI-31 Prepare course advertisement hoardings for event venue	Medium	DD Divya G D	Unassigned			
VAI-30 Produce and distribute event flier — print and digital	Medium	DD Divya G D	Unassigned			
VAI-40 Get Director sign-off on final flier design before print production	Medium	DD Divya G D	Unassigned			
VAI-29 Plan entertainment, refreshments, and draft prize amounts	Medium	DD Divya G D	Unassigned			

Epic 3 expanded — VAI-25 through VAI-38 + subtasks VAI-39 to VAI-42. Full event execution lifecycle across Sprints 6 (Plan & Logistics) and 7 (Execute & Review).

Epic 4 — Partner Workshops & Placement Pipeline

10 stories + 3 subtasks across Sprints 8–9. Formalization of Snappy Lime hiring agreement, Sripada Studios placement MoU (with student profile template subtask), RG Institute workshop scheduling and delivery (3-day: 50 students; 6-day: 30 students), 15-day conversion offer, and outcome tracking.

Outcome: 21.25% workshop-to-enrolment conversion (17 of 80 attendees). Conversion report prepared for Director review. Placement pipeline activated via Snappy Lime (hiring collaboration) and Sripada Studios (placement partnership).

Note on chronology: Epic 4 groups four workstreams that span Feb 2023 to mid-2025 — the RG Institute workshop deliveries (Feb 2023) predate every other epic, while the Snappy Lime (Oct 2024) and Sripada Studios (Jan 2025) formalisations actually predate Cinemotsava 2025 (Sprint 7). The epic is structured around the workstream "Partner ecosystem & placement," not around a strict time window; sprint numbers reflect Jira portfolio sequencing, not real-world chronology. RG Institute workshops were the seed event; partnership formalisations were back-built into the same epic to consolidate the placement pipeline storyline.

VAI board

Q Search wo...

DD

CK

Filter

Group

Saved filters

☐	Work	Priority	Reporter	Assignee	
☐	VAI-4 Partner College Workshops & Industry Placement Pipeline	Medium	DD Divya G D	DD Divya G D	
☐	VAI-55 Retrospective — workshop model evaluation and future college expansion plan	Medium	DD Divya G D	Unassigned	
☐	VAI-54 Track placement outcomes via Sripada Studios and Snappy Lime pipelines	Medium	DD Divya G D	Unassigned	
☐	VAI-52 Track workshop-to-enrolment conversions and report outcomes	Medium	DD Divya G D	Unassigned	
☐	VAI-53 Prepare conversion report with course-wise breakdown for Director review meeting	Medium	DD Divya G D	Unassigned	
☐	VAI-51 Launch 15-day conversion offer for workshop attendees	Medium	DD Divya G D	Unassigned	
☐	VAI-50 Deliver 6-day workshop batch at RG Institute — 30 students	Medium	DD Divya G D	Unassigned	
☐	VAI-49 Deliver 3-day workshop batch at RG Institute — 50 students	Medium	DD Divya G D	Unassigned	
☐	VAI-47 Establish RG Institute partnership and schedule first workshop	Medium	DD Divya G D	Unassigned	
☐	VAI-48 Coordinate with Sunil to confirm lab hours and infrastructure readiness at RG Institute	Medium	DD Divya G D	Unassigned	
☐	VAI-46 Design workshop curriculum and pricing model for partner colleges	Medium	DD Divya G D	Unassigned	
☐	VAI-44 Formalize Sripada Studios official placement partner agreement	Medium	DD Divya G D	Unassigned	
☐	VAI-45 Draft student profile sharing template for Sripada Studios shortlisting process	Medium	DD Divya G D	Unassigned	
☐	VAI-43 Formalize Snappy Lime hiring collaboration agreement	Medium	DD Divya G D	Unassigned	

+ Create

4 of 4

Epic 4 expanded — VAI-43 through VAI-55 + subtasks covering partnership formalization, workshop delivery, conversion tracking, and retrospective planning.

Section 4: Jira Delivery Reports

Velocity Chart — All 9 Sprints

Sprints 5–9 show active velocity (23, 17, 15, 11, 18 story points respectively). Sprints 1–4 show zero — a known limitation of retrospective documentation where story points were backfilled after sprint close. Jira snapshots velocity at close time; retroactive updates don't recalculate historical bars. The underlying data is accurate (see Sprint Summary Table).



Sprint	Commitment	Completed
Sprint 1 — Semester Pre-Launch	0	0
Sprint 2 — Enrolment & Launch	0	0
Sprint 3 — Semester Retrospect	0	0
Sprint 4 — Content & Design	0	0
Sprint 5 — Review & Launch	0	23
Sprint 6 — Plan & Logistics	0	17
Sprint 7 — Execute & Review	0	15
Sprint 8 — Partners & Plan	0	11
Sprint 9 — Deliver & Convert	0	18

Sprint Summary Table — all 9 sprints. Commitment shows 0 for all (retrospective documentation artefact). Completed: Sprints 5–9 show 23, 17, 15, 11, 18 points respectively. 100% completion rate across Sprints 5–9.

Sprint 4 — Brochure Content & Design (Lesson Learned)

Sprint Report

▼How to read this chart

...

...

Sprint 4 — Content & Design ▼

Closed sprint, ended by Divya G D 01/Aug/24 5:33 PM - 31/Mar/26 5:35 PM [View linked pages](#)
Content extracted from all 7 programmes, design brief delivered to external designer, Draft 1 in production



Sprint 4 burndown: flat line across the sprint duration with a steep drop at the right edge — characteristic of retrospective batch-completion. Sprint ran Aug 2024 – Mar 2026 due to retroactive date assignment.

Status Report

* Issue added to sprint after start time

Issues Not Completed [View in Issue Navigator](#)

Key	Summary	Issue Type	Priority	Status	Story Points (8)
VAI-15 *	Extract curriculum content — all 7 programmes via 1-1 sessions with Chethan Kumar	☒ Story	Medium	IN REVIEW	8

Issues completed outside of this sprint [View in Issue Navigator](#)

Key	Summary	Issue Type	Priority	Status	Story Points (3)
VAI-16 *	Draft design brief and brief external designer	☒ Story	Medium	IN PROGRESS	3

Sprint 4 Status Report: VAI-15 (IN REVIEW, 8 pts) listed as 'Issues Not Completed'; VAI-16 (IN PROGRESS, 3 pts) as 'Issues completed outside of this sprint.' Both are DONE in current board view. Root cause: status transitions happened after sprint close. See Bug 6, Section 6.

Sprint 9 — Workshops Delivery & Convert (Clean Completion)


Spaces / Vistara — Programme Delivery & Events / VAI board / Reports

Sprint Report

How to read this chart

How to read this chart

Understand the work completed or pushed back to the backlog in each sprint. This helps you determine if your team is overcommitting or if there is excessive scope creep.

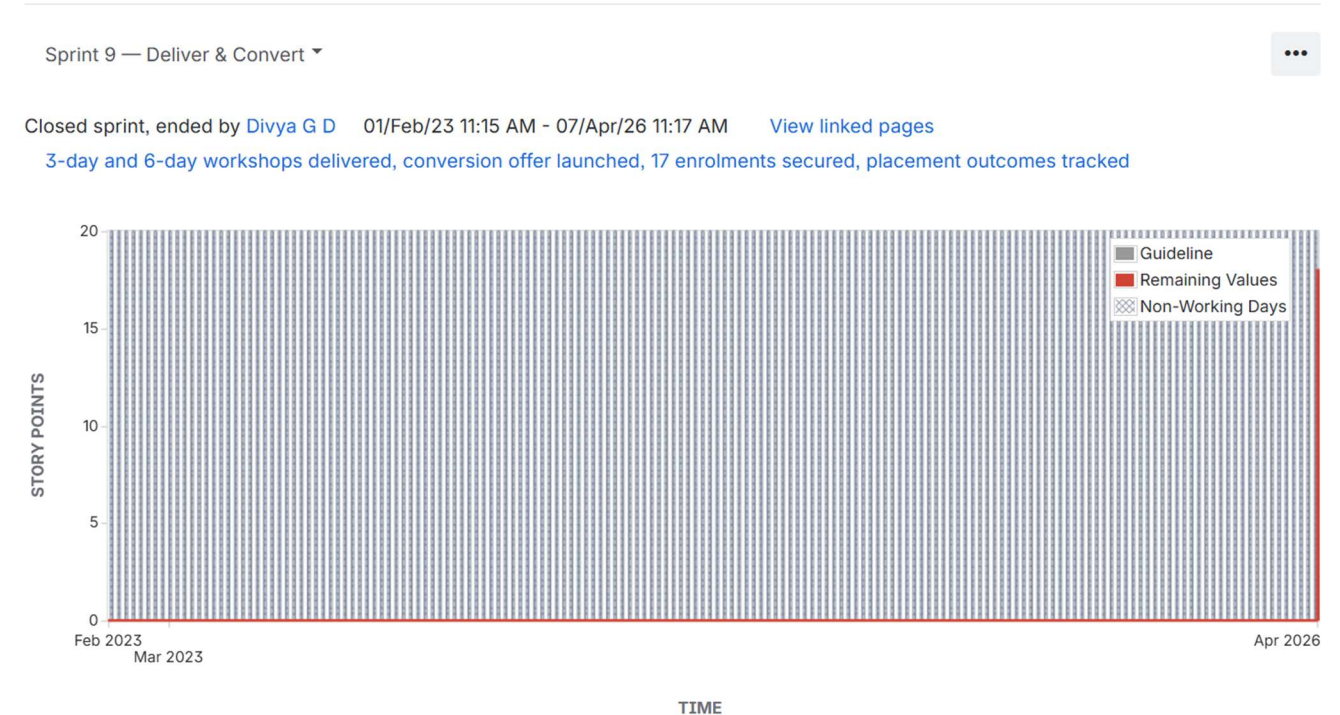

Sprint 9 burndown: Feb 2023 – Apr 2026 timeline (retroactive dates). All 18 story points committed; steep drop at right edge confirms batch completion on close.

Status Report

* Issue added to sprint after start time

Completed Issues

View in Issue Navigator

Key	Summary	Issue Type	Priority	Status	Story Points (18)
VAI-49 *	Deliver 3-day workshop batch at RG Institute — 50 students	Story	Medium	DONE	3
VAI-50 *	Deliver 6-day workshop batch at RG Institute — 30 students	Story	Medium	DONE	5
VAI-51 *	Launch 15-day conversion offer for workshop attendees	Story	Medium	DONE	2
VAI-52 *	Track workshop-to-enrolment conversions and report outcomes	Story	Medium	DONE	3
VAI-54 *	Track placement outcomes via Sripada Studios and Snappy Lime pipelines	Story	Medium	DONE	3
VAI-55 *	Retrospective — workshop model evaluation and future college expansion plan	Story	Medium	DONE	2

Sprint 9 Status Report: all 6 stories DONE, 18 story points delivered. * indicates issues added after sprint start (expected in retrospective flow). Stories cover 3-day workshop, 6-day workshop, conversion offer, outcome tracking, placement tracking, and retrospective.

Epic 3 Burndown — Cinemotsava 2025

Spaces / Vistara — Programme Delivery & Events / VAI board / Reports


Epic Burndown

How to read this chart



VAI-3: Cinemotsava 2025 — Annual Film & Gaming E... [View linked pages](#)

0% unestimated issues 32 of 32 completed (story points)

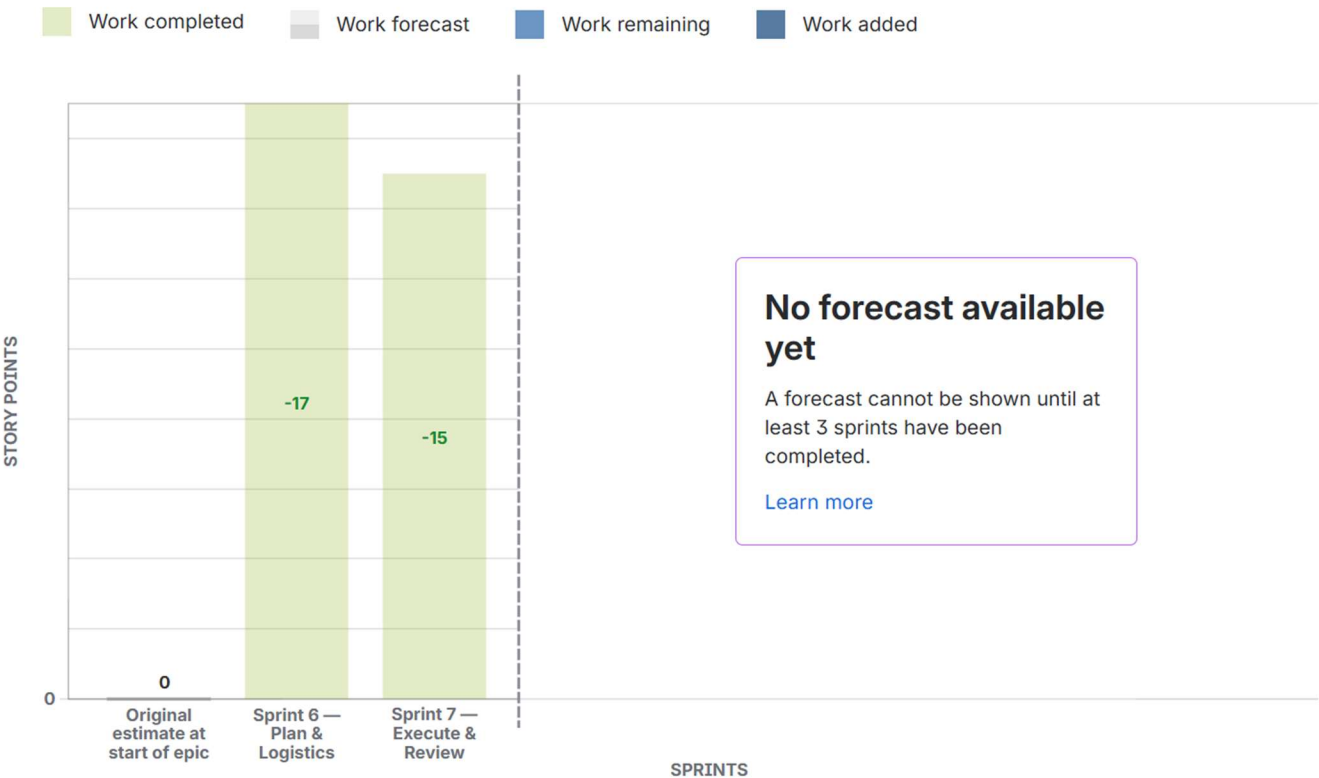

Epic 3 burndown: 32 of 32 story points completed. 0% unestimated issues. Sprint 6 (Plan & Logistics) burned -17 pts; Sprint 7 (Execute & Review) burned -15 pts. No forecast available — requires 3+ completed sprints on the epic (only 2 sprints in scope).

Epic Burndown

How to read this chart

Sprint 7 — Execute & Review 01/Feb/25 - 05/Apr/26

[View in Issue Navigator](#)

Key	Summary	Issue Type	Priority	Status	Story Points (15)
VAI-32	Invite GMIT lecturers and HoDs as event attendees	☒ Story	Medium	DONE	1
VAI-33	Invite industry partners as guests of honour	☒ Story	Medium	DONE	1
VAI-34	Finalize prize amounts based on registration count	☒ Story	Medium	DONE	1
VAI-35	Prepare event grounds and coordinate caterers — weekend setup	☒ Story	Medium	DONE	2
VAI-36	Execute Cinemotsava event day — Feb 12, 2025	☒ Story	Medium	DONE	5
VAI-37	Post-event analysis — track admission conversions across 7 courses	☒ Story	Medium	DONE	3
VAI-38	Post-event retrospective and next-event planning	☒ Story	Medium	DONE	2

Sprint 6 — Plan & Logistics 06/Jan/25 - 05/Apr/26

[View in Issue Navigator](#)

Key	Summary	Issue Type	Priority	Status	Story Points (17)
VAI-25	Finalize event collaboration with Vishistaa Cine Journey	☒ Story	Medium	DONE	3
VAI-26	Secure venue approval from GMIT Principal and confirm event date	☒ Story	Medium	DONE	2
VAI-27	Define budget, registration fee, and competition structure	☒ Story	Medium	DONE	3
VAI-29	Plan entertainment, refreshments, and draft prize amounts	☒ Story	Medium	DONE	2
VAI-28	Finalize registration POCs and assign on-ground crew roles	☒ Story	Medium	DONE	2
VAI-30	Produce and distribute event flier — print and digital	☒ Story	Medium	DONE	3
VAI-31	Prepare course advertisement hoardings for event venue	☒ Story	Medium	DONE	2

Epic 3 story-by-story completion: all 14 stories DONE across Sprints 6–7. Points range from 1 (low-effort invites) to 5 (VAI-36 — event execution day).

VAI-36 — Story Detail: Execute Cinemotsava Event Day

VAI-36 is the highest-effort story in the portfolio (5 points) and represents the climactic execution of Cinemotsava 2025. The detail view below demonstrates the full story structure used across the portfolio.

Execute Cinemotsava event day — Feb 12, 2025



Description

As PM and sole event coordinator, I need to manage all on-ground operations on event day so that competitions run on schedule, guests are hosted professionally, and attendees have a seamless experience.

Subtasks

Work	Pri...	Stor...	As...	Status
VAI-41 Manage competition judging and winner selection	M		U	DONE
VAI-42 Coordinate guest of honour arrival, introduction, and hospitality	M		U	DONE

Linked work items

Add linked work item

Activity

Add a comment...

Looks good! Need help? This is blocked... Can you clarify...?

Pro tip: press **M** to comment

Details

Due date	None
Start date	None
Story point estimate	None
Story Points	5
Sprint	None +1
Priority	Medium
Parent	VAI-3 Cinemotsava 2025

Development

More fields Original estimate, Time tracking, Component...

Automation Rule executions

Created April 1, 2026 at 4:32 PM

Updated last week

Resolved last week

Configure

VAI-36 detail: user-story description, two subtasks (VAI-41 competition judging, VAI-42 guest of honour coordination — both DONE), Story Points = 5, Parent epic VAI-3. Note: 'Story point estimate' sidebar field shows None — this is customfield_10016 (not used). Actual story points are stored in customfield_10037 (see Bug 1, Section 6).

introduction, and hospitality

Linked work items

Add linked work item

Activity

All Comments History Work log

Add a comment...

Looks good! Need help? This is blocked... Can you clarify...?

Pro tip: press **M** to comment

DD Divya G D
April 1, 2026 at 4:33 PM

Acceptance Criteria:

1. Registration desk operational — attendee check-in running smoothly
2. Competitions executed on schedule — Short Movie, Creative Reels, Gaming events completed
3. Judges coordinated — scoring and winner selection completed without delays
4. Guests of honour hosted — Snappy Lime and other guests received and acknowledged
5. Prize distribution completed — all 5 categories awarded
6. Refreshments served on time — caterer delivery matched attendee flow
7. No P1 incidents — no major disruptions to event schedule

1

Details

Due date	None
Start date	None
Story point estimate	None
Story Points	5
Sprint	None +1
Priority	Medium
Parent	VAI-3 Cinemotsava 2025

Development

More fields Original estimate, Time tracking, Component...

Automation Rule executions

Created April 1, 2026 at 4:32 PM

Updated last week

Resolved last week

Configure

VAI-36 Acceptance Criteria — posted as ADF-formatted comment by Divya G D, April 1, 2026. 7 criteria covering registration desk operations, competition scheduling, judging, guest hospitality, prize distribution, catering, and P1-free delivery.

VAI board

< Back

VAI-3 / VAI-36

^

v

DD

Divya G D created the Work item

April 1, 2026 at 4:32 PM

DD

Divya G D changed the Parent

April 1, 2026 at 4:32 PM

None → VAI-3

DD

Divya G D updated the Sprint

April 1, 2026 at 4:33 PM

None → Sprint 7 — Execute & Review

DD

Divya G D changed the Status

last week

TO DO → IN PROGRESS

DD

Divya G D changed the Status

last week

IN PROGRESS → IN REVIEW

DD

Divya G D updated the Resolution

last week

None → Done

DD

Divya G D changed the Status

last week

IN REVIEW → DONE

DD

Divya G D created the Work item

1 minute ago

1

...

Details

Due date

None

Start date

None

Story point estimate

None

Story Points

5

Sprint

None +1

Priority

Medium

Parent

VAI-3 Cinemotsava 2025

Development

More fields

Original estimate, Time tracking, Component...

Automation

Rule executions

Created April 1, 2026 at 4:32 PM

Updated last week


Resolved last week

Configure

VAI-36 History / Audit Trail: full lifecycle visible — created Apr 1 at 4:32 PM, parent set to VAI-3, sprint assigned to Sprint 7, status transitions TO DO → IN PROGRESS → IN REVIEW → DONE, resolution set to Done.

Section 5: Confluence Documentation

Confluence documentation covers two trees: (1) the Animation Programme Launch (BIET) project space with 6 supporting pages — originally created under the working title ‘GM University x Vistara’ anticipating the B.Sc. expansion, and repurposed for the BIET launch when that arrangement remained pending; and (2) the Vistara Programme Portfolio — Product Operations Hub with PRD, Roadmap, Strategic Plan, and 1-1 Meeting Notes.

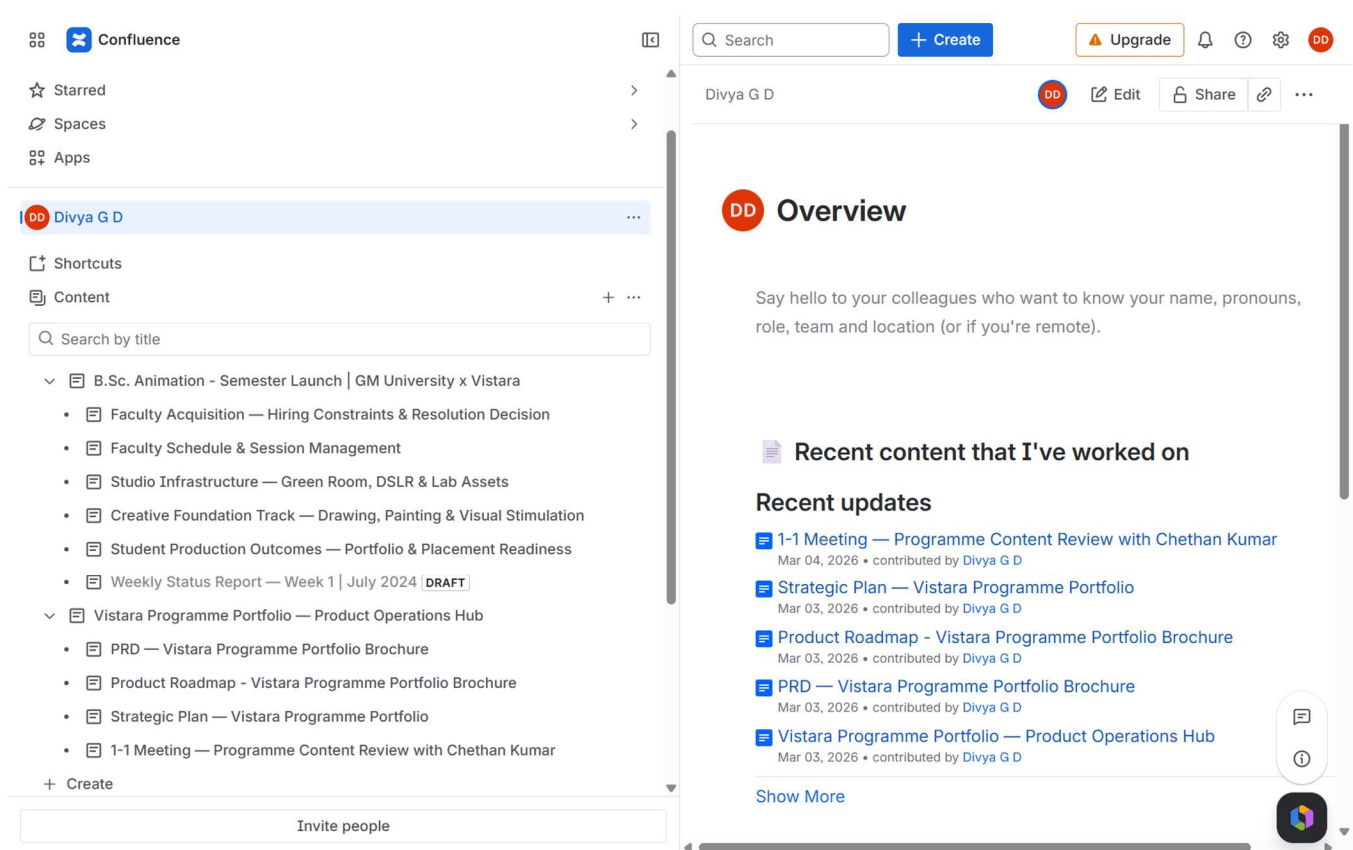

Confluence workspace — both documentation trees fully expanded. Left sidebar shows complete page hierarchy. Recent updates timestamps confirm active documentation from March–April 2026.

PRD — Vistara Programme Portfolio Brochure

The PRD documents the 8-programme go-to-market brochure as a product. It covers the product objective, all 8 programmes with durations, success metrics, design specifications, and stakeholder sign-off process. The actual brochure PDF is attached directly in the Designs section.

By Divya G D 3 min See views Add a reaction

Product overview	
Target date	5 - September - 2024
Document status	COMPLETE
Team members	@Divya G D @Chethan Kumar @Dinesh G K
Quick links	
Designs	Brochure.pdf 11 Apr 2026, 03:52 PM
Work tracker	VAI-2: Brochure Production — Programme Portfolio DONE

Objective

The Vistara Programme Portfolio Brochure is a go-to-market collateral product designed to communicate the institute's full programme offering to prospective students, institutional partners, and placement contacts. The brochure serves as the primary decision-making tool for students evaluating programme enrolment, and as a credibility document for university and government

PRD overview table: Target date Sep 5, 2024, Document status COMPLETE, Team: Divya G D, Chethan Kumar, Dinesh G K. Brochure.pdf attached in Designs section. VAI-2 work tracker linked as DONE — demonstrating Jira–Confluence integration via web link (free-tier workaround).

Objective

The Vistara Programme Portfolio Brochure is a go-to-market collateral product designed to communicate the institute's full programme offering to prospective students, institutional partners, and placement contacts. The brochure serves as the primary decision-making tool for students evaluating programme enrolment, and as a credibility document for university and government partnership discussions.

This brochure was the first formal go-to-market collateral produced after Vistara Animation's transition to OPC Pvt. Ltd. structure (CIN: U85500KA2024OPC188895), launched September 2024 to support the institute's enrolment outreach across GM University, BIET, and the Sripada Studios placement pipeline.

This PRD governs the content requirements, design specifications, and stakeholder sign-off process for the brochure covering all 8 programmes:

- **AVEP** — Advance Video Editing Program (6 months)
- **DMP** — Design in Multimedia Program (6 months)
- **Maya Plus** — 3D Animation specialization (6 months)
- **3D Prime** — 3D Modeling, Texturing & Lighting (16 months)
- **Certificate in 3DS Max Architecture & Design** (1 year)
- **GWD** — Graphic & Web Designing (1 year 2 months)
- **AVP** — Advance Visual Effects (2 years)
- **VAAVP** — Vistara Advance Animation & Visual Effects Program (3 years)

Success metrics

PRD Objective section: all 8 programmes listed with full names and durations — AVEP (6mo), DMP (6mo), Maya Plus (6mo), 3D Prime (16mo), 3DS Max Architecture (1yr), GWD (1yr 2mo), AVP (2yr), VAAVP (3yr). Context paragraph notes OPC registration (May 2024) and enrolment outreach scope.

Confluence Scope Decision

Confluence pages for Epics 2–4 were scoped out after a confirmed API restriction blocked programmatic page creation in free-tier personal spaces (Bug 8). The decision was deliberate: the existing PRD and project documentation pages demonstrate Confluence proficiency at the level required for PM portfolio purposes. Manual creation of 8–10 additional pages was deprioritised in favour of completing the Jira structure and agent work.


Section 6: The AI Agent — Technical Build

The portfolio was not built manually through the Jira UI. A custom Python agent was developed from scratch to automate the creation of epics, stories, subtasks, sprint assignments, acceptance criteria, and story point configuration — using the Jira REST API and Anthropic Claude API.

Agent Architecture


Execution flow: Script reads spec → (Optional) Claude API enriches descriptions → Jira REST API creates Epics → Stories → Subtasks → Sprint assignments → Acceptance criteria comments → Story point updates → Confluence pages linked via web links

Repository Structure

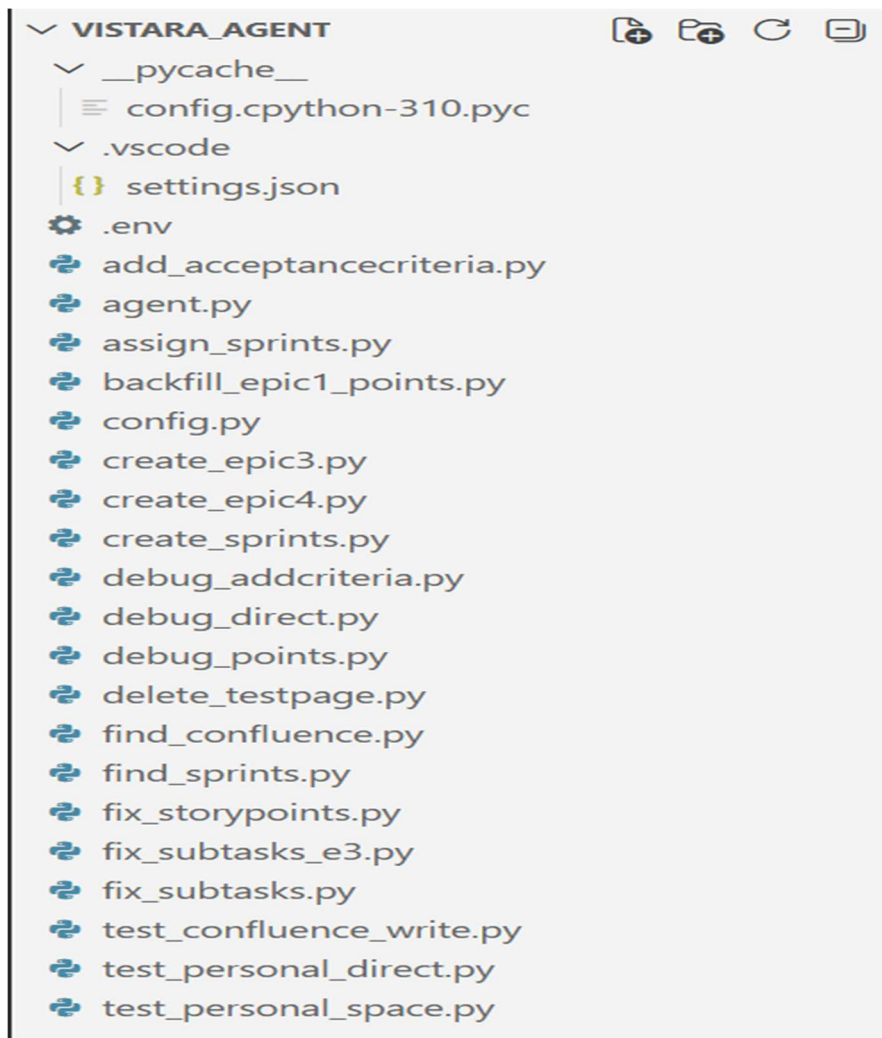

VS Code file explorer: VISTARA_AGENT project folder showing all agent scripts, config files, .env, and test/debug utilities. 20+ files built across the project lifecycle.

Core Script — create_epic3.py (ADF Payload)

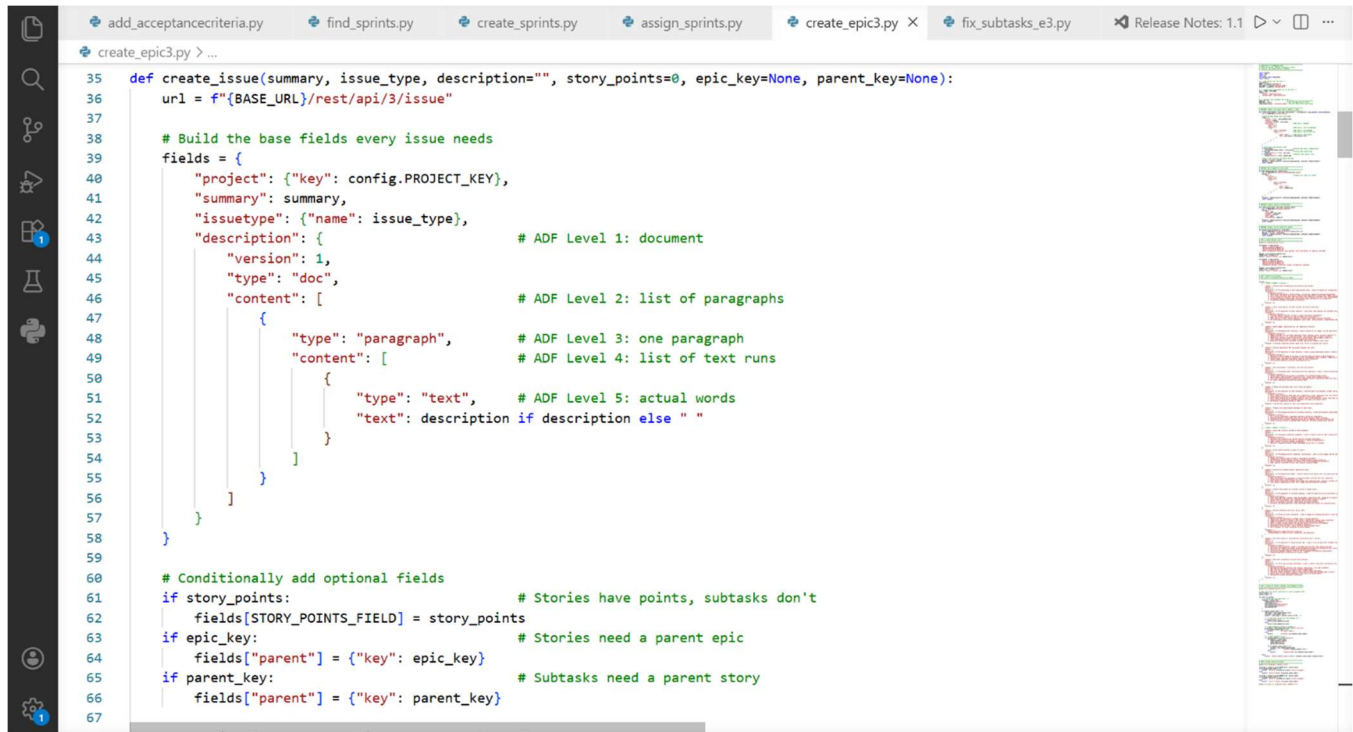

```
35 def create_issue(summary, issue_type, description="", story_points=0, epic_key=None, parent_key=None):
36     url = f"{BASE_URL}/rest/api/3/issue"
37
38     # Build the base fields every issue needs
39     fields = {
40         "project": {"key": config.PROJECT_KEY},
41         "summary": summary,
42         "issuetype": {"name": issue_type},
43         "description": {
44             "version": 1,
45             "type": "doc",
46             "content": [
47                 {
48                     "type": "paragraph",
49                     "content": [
50                         {
51                             "type": "text",
52                             "text": description if description else " "
53                         }
54                     ]
55                 }
56             ]
57         }
58     }
59
60     # Conditionally add optional fields
61     if story_points:
62         fields[STORY_POINTS_FIELD] = story_points
63     if epic_key:
64         fields["parent"] = {"key": epic_key}
65     if parent_key:
66         fields["parent"] = {"key": parent_key}
```

create_epic3.py lines 35–67: the create_issue() function showing 5-level ADF nesting for description fields (doc → content → paragraph → content → text). Conditional logic for story points, epic parent, and subtask parent using the same 'parent' field. Comments explain each ADF level inline.

Configuration — config.py + .env

The screenshot shows the VS Code interface for the `vistara_agent` project. The Explorer panel on the left lists the project files, including `config.py`. The main editor displays the `config.py` file with the following constants:

```
1 PROJECT_KEY = "VAI"  
2 EPIC_ISSUE_TYPE = "Epic"  
3 STORY_ISSUE_TYPE = "Story"  
4 SUBTASK_ISSUE_TYPE = "Subtask"
```

The Terminal panel at the bottom shows the output of the `find_sprints.py` script. It identifies the VAI board with ID 100 and lists all 9 sprints with their IDs and states:

```
(vistara-agent) C:\Users\divya\OneDrive\Documents\Agentic PM\vistara_agent>python find_sprints.py  
Board: VAI board | ID: 100  
Board: PROJ board | ID: 34  
Board: PRJ board | ID: 67  
  
=== Sprints for VAI board ===  
  
Sprint 1 - Semester Pre-Launch | ID: 70 | State: closed  
Sprint 2 - Enrolment & Launch | ID: 103 | State: closed  
Sprint 3 - Semester Retrospect | ID: 104 | State: closed
```

config.py (left panel): PROJECT_KEY='VAI', issue type constants. Terminal (bottom): find_sprints.py output — discovers VAI board ID: 100, lists all 9 sprints with IDs and states. This discovery script was run before any sprint assignment to confirm correct IDs.

The screenshot shows the VS Code interface for the `vistara_agent` project. The Explorer panel on the left lists the project files, including `.env`. The main editor displays the `.env` file with the following environment variables:

```
1 JIRA_API_TOKEN=ATATT3xFfGf0xUIM7dvud0ITiXtqJXeliULvWTSR5Zx1Pv53bT1_HmYFe75oyWj2Z7Z1h1Z63NI7cJ7NINEvx...  
2 JIRA_EMAIL=divyagdinesh@gmail.com  
3 JIRA_BASE_URL=https://divyagdinesh-software.atlassian.net
```

The Terminal panel at the bottom shows an error message:

```
The process cannot access the file because it is being used by another process.  
The system cannot find the file C:\Users\divya\AppData\Local\Temp\__conda_tmp_26538.txt.  
Failed to run 'conda activate'.  
C:\Users\divya\AppData\Local\Temp\__conda_tmp_26538.txt  
The process cannot access the file because it is being used by another process.  
The system cannot find the file C:\Users\divya\AppData\Local\Temp\__conda_tmp_30848.txt.  
Failed to run 'conda activate vistara-agent'.  
C:\Users\divya\AppData\Local\Temp\__conda_tmp_30848.txt  
C:\Users\divya\OneDrive\Documents\Agentic PM\vistara_agent>
```

.env file structure: JIRA_API_TOKEN (truncated for security), JIRA_EMAIL, JIRA_BASE_URL. Loaded at runtime via python-dotenv — token never hardcoded in scripts.

Successful Agent Run — Sprint Assignment

```
(vistara-agent) C:\Users\divya\OneDrive\Documents\Agentic PM\vistara_agent>python assign_sprints.py  
Sprint 170 – assigned ['VAI-15', 'VAI-16']  
Sprint 171 – assigned ['VAI-17', 'VAI-18', 'VAI-19', 'VAI-20', 'VAI-21', 'VAI-22']
```

assign_sprints.py successful execution: Sprint 170 assigned VAI-15, VAI-16 (Sprint 4). Sprint 171 assigned VAI-17 through VAI-22 (Sprint 5). Clean output confirms correct sprint IDs and story keys.

Section 7: Learnings & Debugging Journey

Eight bugs were encountered, diagnosed, and resolved during the portfolio build. Each is documented with root cause, fix, and lesson — both as a transparency note on retrospective documentation and as evidence of structured debugging discipline.


Bug 1 — Story Points Field Mismatch

Symptom: Story points written via agent showed 0 in Jira UI across all stories.

Root cause: Agent wrote to customfield_10016 (Jira default / 'Story point estimate'). This instance stores user-facing story points in customfield_10037 ('Story Points').

Fix: Built debug_points.py to identify correct field via GET /rest/api/3/field. Bulk-updated all stories via fix_storypoints.py using HTTP PUT.

Lesson: Always run field discovery on a new Jira instance before bulk writes. Default field IDs are not universal.

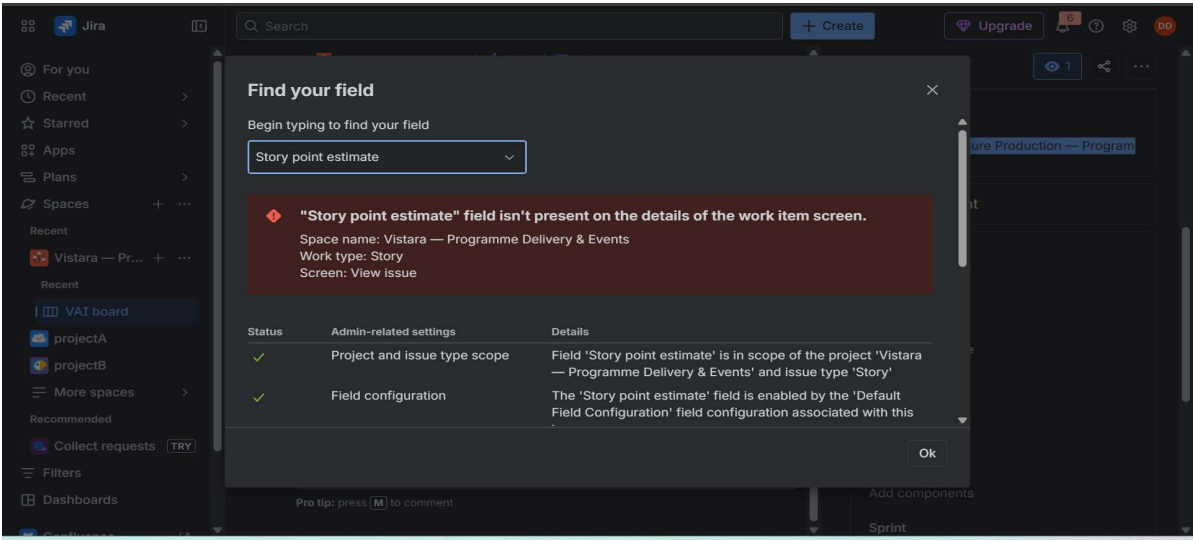

Jira 'Find your field' dialog: 'Story point estimate' field (customfield_10016) is in scope and configured — but NOT present on the View Issue screen. This confirms why agent writes to 10016 were silently accepted but never displayed. customfield_10037 is the correct field for this instance.

```
8 EMAIL = os.getenv("JIRA_EMAIL")
9 API_TOKEN = os.getenv("JIRA_API_TOKEN")
10 BASE_URL = os.getenv("JIRA_BASE_URL")
11
12 auth = (EMAIL, API_TOKEN)
13 headers = {"Accept": "application/json"}
14
15 # Step 1: Get ALL fields from Jira to find story point fields
16 print("=== Finding all story point related fields ===\n")
17 url = f"{BASE_URL}/rest/api/3/field"
18 response = requests.get(url, auth=auth, headers=headers)
19 fields = json.loads(response.text)
20
21 for field in fields:
22     name = field["name"].lower()
23     if "point" in name or "estimate" in name or "story" in name:
24         print(f"    Name: {field['name']}")
25         print(f"    ID: {field['id']}")
26         print(f"    Type: {field.get('schema', {}).get('type', 'unknown')}")
27         print()
28
29 # Step 2: Check VAI-15 values for those fields
30 print("=== VAI-15 current values ===\n")
31 url2 = f"{BASE_URL}/rest/api/3/issue/VAI-15"
32 response2 = requests.get(url2, auth=auth, headers=headers)
33 data = json.loads(response2.text)
34
35 for field in fields:
36     name = field["name"].lower()
37     if "point" in name or "estimate" in name or "story" in name:
38         field_id = field["id"]
39         value = data["fields"].get(field_id, "NOT IN RESPONSE")
40         print(f"    {field['name']} ({field_id}) = {value}")
```

debug_points.py code: lines 15–40 showing the field discovery logic — GET all fields from Jira, filter by 'point/estimate/story' in name, then check VAI-15's actual values for each matching field. This identified customfield_10037 as the correct target.

```
(vistara-agent) C:\Users\divya\OneDrive\Documents\Agentic PM\vistara_agent>python debug_points.py
=== Finding all story point related fields ===

Name: Story Points
ID: customfield_10037
Type: number

Name: Story point estimate
ID: customfield_10016
Type: number

Name: Remaining Estimate
ID: timeestimate
Type: number

Name: Σ Original Estimate
ID: aggregatetimeoriginalestimate
Type: number

Name: Original estimate
ID: timeoriginalestimate
Type: number

Name: Σ Remaining Estimate
ID: aggregatetimestimate
Type: number

=== VAI-15 current values ===

Story Points (customfield_10037) = None
Story point estimate (customfield_10016) = 8.0
Remaining Estimate (timeestimate) = None
Σ Original Estimate (aggregatetimeoriginalestimate) = None
Original estimate (timeoriginalestimate) = None
Σ Remaining Estimate (aggregatetimestimate) = None

(vistara-agent) C:\Users\divya\OneDrive\Documents\Agentic PM\vistara_agent>python fix_storypoints.py
```

Terminal output: debug_points.py run shows Story Points (customfield_10037) = None and Story point estimate (customfield_10016) = 8.0 for VAI-15 — confirming the mismatch. fix_storypoints.py run follows immediately, bulk-updating all stories to the correct field.

Bug 2 — Subtask Issue Type Rejection

Symptom: Subtask creation returned 400 errors — issue type not found.

Root cause: Script used 'Subtask' (no hyphen). This Jira instance requires 'Sub-task' (hyphenated). Visible in the early config.py screenshot as SUBTASK_ISSUE_TYPE = 'Subtask'.

Fix: Updated issue type string to 'Sub-task' across all creation scripts.

Lesson: Issue type names are instance-configured. Verify via GET /rest/api/3/issuetype before building creation scripts.


Bug 3 — API Token Expiration Mid-Session

Symptom: All API calls returning 404 simultaneously — including endpoints that had worked earlier in the same session.

Root cause: The vistara-agent token expired mid-build. Atlassian returns 404 (not 401) for expired token calls — making this non-obvious to diagnose.

Fix: Generated new token vistara-agent-2 (expires Apr 30, 2026). Updated .env. All calls resumed.

Lesson: Atlassian's 404 on expired tokens is misleading. When all endpoints fail simultaneously, check token validity first.

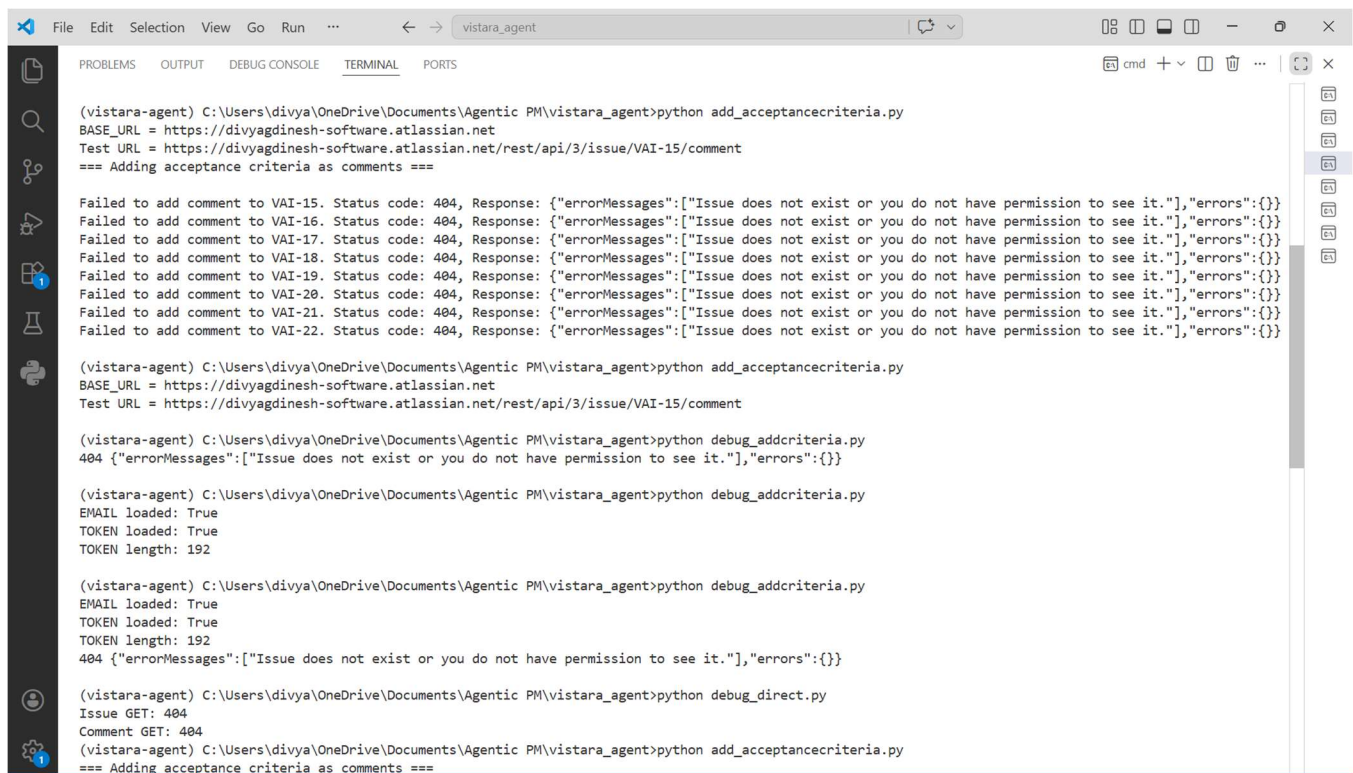

```
(vistara-agent) C:\Users\divya\OneDrive\Documents\Agentic PM\vistara_agent>python add_acceptancecriteria.py
BASE_URL = https://divyagdinesh-software.atlassian.net
Test URL = https://divyagdinesh-software.atlassian.net/rest/api/3/issue/VAI-15/comment
=== Adding acceptance criteria as comments ===

Failed to add comment to VAI-15. Status code: 404, Response: {"errorMessages":["Issue does not exist or you do not have permission to see it."],"errors":{}}
Failed to add comment to VAI-16. Status code: 404, Response: {"errorMessages":["Issue does not exist or you do not have permission to see it."],"errors":{}}
Failed to add comment to VAI-17. Status code: 404, Response: {"errorMessages":["Issue does not exist or you do not have permission to see it."],"errors":{}}
Failed to add comment to VAI-18. Status code: 404, Response: {"errorMessages":["Issue does not exist or you do not have permission to see it."],"errors":{}}
Failed to add comment to VAI-19. Status code: 404, Response: {"errorMessages":["Issue does not exist or you do not have permission to see it."],"errors":{}}
Failed to add comment to VAI-20. Status code: 404, Response: {"errorMessages":["Issue does not exist or you do not have permission to see it."],"errors":{}}
Failed to add comment to VAI-21. Status code: 404, Response: {"errorMessages":["Issue does not exist or you do not have permission to see it."],"errors":{}}
Failed to add comment to VAI-22. Status code: 404, Response: {"errorMessages":["Issue does not exist or you do not have permission to see it."],"errors":{}}

(vistara-agent) C:\Users\divya\OneDrive\Documents\Agentic PM\vistara_agent>python add_acceptancecriteria.py
BASE_URL = https://divyagdinesh-software.atlassian.net
Test URL = https://divyagdinesh-software.atlassian.net/rest/api/3/issue/VAI-15/comment

(vistara-agent) C:\Users\divya\OneDrive\Documents\Agentic PM\vistara_agent>python debug_addcriteria.py
404 {"errorMessages":["Issue does not exist or you do not have permission to see it."],"errors":{}}

(vistara-agent) C:\Users\divya\OneDrive\Documents\Agentic PM\vistara_agent>python debug_addcriteria.py
EMAIL loaded: True
TOKEN loaded: True
TOKEN length: 192

(vistara-agent) C:\Users\divya\OneDrive\Documents\Agentic PM\vistara_agent>python debug_addcriteria.py
EMAIL loaded: True
TOKEN loaded: True
TOKEN length: 192
404 {"errorMessages":["Issue does not exist or you do not have permission to see it."],"errors":{}}

(vistara-agent) C:\Users\divya\OneDrive\Documents\Agentic PM\vistara_agent>python debug_direct.py
Issue GET: 404
Comment GET: 404

(vistara-agent) C:\Users\divya\OneDrive\Documents\Agentic PM\vistara_agent>python add_acceptancecriteria.py
=== Adding acceptance criteria as comments ===
```

Terminal: complete Bug 3 narrative in one frame. Top: 404 cascade across VAI-15 to VAI-22 on add_acceptancecriteria.py. Middle: debug_addcriteria.py confirms 404 with token length 192. Bottom: after new token generated — 'Added acceptance criteria comment to VAI-15 through VAI-22' — all 8 succeed.

ATLASSIAN Account

[Profile and visibility](#)
[Email](#)
[Security](#)
[Privacy](#)
[Account preferences](#)
[Connected apps](#)
[More](#)

API Tokens

[Create API token](#)
[Create API token with scopes](#)
[Revoke all API tokens](#)

Your API tokens need to be treated as securely as any other password. You can only create a maximum of 25 tokens at a time.

New tokens may take up to a minute to work after they've been created.

Token name	Created	Expires	Last accessed	Action
vistara-agent	Mar 9, 2026	Expired Mar 31, 2026	3 days ago	Revoke
H2O	Dec 2, 2025	Expired Dec 9, 2025	119 days ago	Revoke

Atlassian API Tokens page (Mar 31, 2026): vistara-agent token showing 'Expired Mar 31, 2026' — confirms the expiry that caused the 404 cascade.

ATLASSIAN Account

[Profile and visibility](#)
[Email](#)
[Security](#)
[Privacy](#)
[Account preferences](#)
[Connected apps](#)
[More](#)

API Tokens

[Create API token](#)
[Create API token with scopes](#)
[Revoke all API tokens](#)

Your API tokens need to be treated as securely as any other password. You can only create a maximum of 25 tokens at a time.

New tokens may take up to a minute to work after they've been created.

Token name	Created	Expires	Last accessed	Action
vistara-agent-2	Mar 31, 2026	Apr 30, 2026	10 minutes ago	Revoke
vistara-agent	Mar 9, 2026	Expired Mar 31, 2026	12 days ago	Revoke
H2O	Dec 2, 2025	Expired Dec 9, 2025	128 days ago	Revoke

Atlassian API Tokens page (Apr 9, 2026): vistara-agent-2 active with expiry Apr 30, 2026. Old expired token still visible for reference. Fix confirmed.

Bug 4 — Sprint Name 30-Character Limit

- Symptom:** Sprint creation returned 400 validation error.
- Root cause:** Sprint names exceeded Jira's 30-character limit.
- Fix:** Shortened all sprint names (e.g. 'Sprint 4 — Content & Design Brief' → 'Sprint 4 — Content & Design').
- Lesson:** Test sprint creation with a short name first. Character limits are not prominently documented.

```
(vistara-agent) C:\Users\divya\OneDrive\Documents\Agentic PM\vistara_agent>python create_sprints.py
FAILED: 400 - {"errorMessages":[],"errors":{"name":"Sprint name must be shorter than 30 characters."}}
```

Terminal: create_sprints.py returning FAILED: 400 — 'Sprint name must be shorter than 30 characters.' Clean, unambiguous error that guided the immediate fix.

Bug 5 — Acceptance Criteria ADF Format Rejection

Symptom: Comment creation returned 400 — invalid body format.

Root cause: Comments posted as plain text strings. Jira REST API v3 requires ADF (Atlassian Document Format) — a 5-level nested JSON structure.

Fix: Rebuilt all comment payloads in ADF format. Built `debug_addcriteria.py` to test structure before bulk run.

Lesson: Jira REST API v3 endpoints require ADF. v2 endpoints accept markdown. Verify API version before building comment payloads.

Bug 6 — Sprint 4 Status Mismatch at Close

Symptom: Sprint 4 report showed 'Issues Not Completed' for VAI-15 and VAI-16 despite both showing Done in current board view.

Root cause: Both stories were transitioned to Done after the sprint was already closed. Sprint reports snapshot statuses at the exact moment of close.

Fix: Accepted as a documentation artefact. Documented rather than masked.

Lesson: In live sprints: always transition stories to Done before closing. Sprint reports are immutable post-close.

Bug 7 — Epic 1 Story Points Missing from Velocity Chart

Symptom: Velocity chart shows 0 for Sprints 1–4 despite story points being set on all stories.

Root cause: Story points for Epics 1–2 were backfilled after sprint close. Jira snapshots velocity at close time — retroactive updates don't recalculate historical velocity.

Lesson: Velocity is a snapshot metric. Backfilling after sprint close produces accurate story data but does not recover historical velocity bars.

Bug 8 — Confluence API Blocked for Personal Spaces

Symptom: Confluence page creation via API returned 403 for personal space URLs.

Root cause: Atlassian free tier restricts programmatic creation of pages in personal (~) spaces. Platform-level restriction, not a configuration issue.

Fix: Epic 1 pages (manually built) retained. Confluence pages for Epics 2–4 scoped out as a deliberate portfolio trade-off.

Lesson: Validate API access permissions at project start — before building scripts. Free-tier restrictions can block entire automation approaches.

Section 8: Enterprise PM Skill Mapping

The table below maps portfolio deliverables to enterprise PM competencies — translating startup operational execution into the language used by delivery organisations, PMOs, and implementation functions.

PM Competency	Portfolio Evidence	Equivalent Skill
Delivery Planning	5-gate semester launch, 2-week cycles, Sprints 1–3	Programme/release planning with defined gates and sprint cadence
Risk Management	Operational risk register; faculty SPOF tracking; infrastructure readiness mitigation; documented in sprint planning and 1-1 notes	Risk log ownership; risk identification and escalation protocols
Stakeholder Management	5-party ecosystem; Director sign-offs; academic MoUs	Multi-party stakeholder management in complex delivery environments
Vendor Management	License procurement lifecycle (Adobe Creative Cloud, Autodesk Maya); partnership agreement management with Snappy Lime and Sripada Studios	Procurement lifecycle and contract management
Event/Programme Delivery	Cinemotsava: Rs. 2L+ budget, 200+ participants, zero on-day P1 incidents, positive stakeholder feedback	Large-scale programme execution with cross-functional coordination
Go-to-Market Execution	8-programme brochure: PRD → design → review → sign-off → multi-channel distribution	Product collateral lifecycle from brief to distribution
Metrics & Reporting	Velocity tracking, burndown analysis, sprint completion rates, conversion tracking	KPI reporting, delivery metrics, sprint/programme health dashboards
Process Improvement	Asset-light infrastructure consolidation (90% rent reduction, Rs. 50K → Rs. 5K); workshop conversion pipeline yielding 21.25% enrolment yield	Operational efficiency initiatives with measurable, organization-wide outcomes
Tool Proficiency	Jira (epics/stories/sprints/reports), Confluence (PRD/charter/roadmap)	Enterprise PM tooling at practitioner level
AI & Automation	Python agent via Jira REST API + Anthropic Claude API — 20 scripts	AI-assisted workflow automation; agentic PM execution

Section 9: GitHub Repository — Build Process via Claude Code

The final step in publishing this portfolio was creating a public GitHub repository containing all 20 agent scripts, documentation, and a structured README. This section documents that process — including the toolchain setup, Claude Code execution, hallucination corrections, and the final verified output.

Repo URL: <https://github.com/divyagowdrudinesh/vistara-pm-agent>

Why GitHub and Why Claude Code

A GitHub repository serves three purposes for this portfolio: (1) it gives interviewers a live, browsable view of the actual code rather than static screenshots; (2) it demonstrates version control discipline — a core expectation in any technical PM or PMO role; and (3) it provides a permanent public URL that can be linked from the resume, LinkedIn, and portfolio document.

Claude Code was chosen over manual setup because it executes directly on the local machine — reading files, running git commands, and pushing to GitHub in a single supervised session. It was run in a second terminal window while this portfolio session ran in parallel, with each step explained in real time.

Toolchain Setup

Three tools required installation before Claude Code could run:

Tool	Purpose / Why Needed
Node.js v24.15.0 LTS	Runtime environment for Claude Code — a JavaScript/TypeScript application. npm (package manager) is bundled with Node.js.
Claude Code v2.1.117	Installed via <code>npm install -g @anthropic-ai/claude-code</code> . Runs in terminal, executes file operations and git commands directly on the machine.
Git for Windows v2.54.0 + Git Bash	Git provides version control commands (init, add, commit, push). Git Bash provides the Unix shell environment Claude Code requires on Windows.


One environment variable was also set to tell Claude Code where Git Bash lives on Windows:

`setx CLAUDE_CODE_GIT_BASH_PATH "C:\Program Files\Git\bin\bash.exe"`

The Prompt Used

The following prompt was pasted into Claude Code after launching it from inside the `vistara_agent` project folder. It specified all 11 steps explicitly to ensure Claude Code executed in a controlled, verifiable sequence rather than making autonomous decisions about structure or content.

I need you to publish my Vistara PM Agent project as a polished GitHub repository. Execute all steps. After each step, print a one-line plain-English summary of what you just did. Details: GitHub username: divyagowdrudinesh | Repo: vistara-pm-agent | Public | MIT license | gh CLI authenticated | Source: C:\Users\divya\OneDrive\Documents\Agentic PM\vistara_agent Steps: (1) Staging directory — copy all .py files, exclude .env/.vscode/.__pycache___. (2) Secret scan — grep for ATATT, JIRA_API_TOKEN=, sk-ant-. Stop if found. (3) .gitignore. (4) .env.example with placeholder values. (5) requirements.txt. (6) Folder structure — show tree and wait for 'confirmed'. (7) README.md with all specified sections. (8) git init and first commit. (9) gh repo create and push. (10) Add topics. (11) Verify .env not in repo, print final URL.

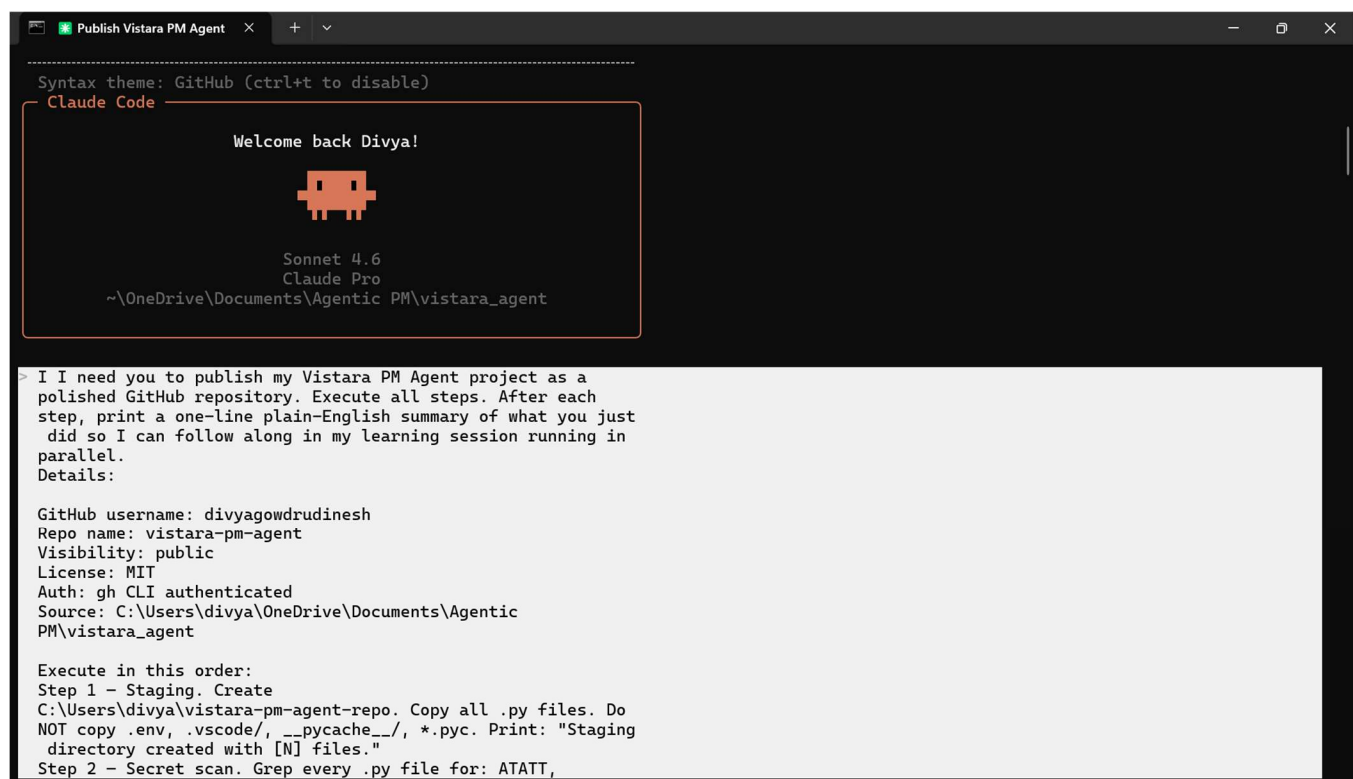

The screenshot shows the Claude Code application window titled "Publish Vistara PM Agent". The top bar indicates the syntax theme is "GitHub (ctrl+t to disable)". The main terminal area displays a welcome message: "Welcome back Divya!" followed by a red robot icon, the version "Sonnet 4.6", the model "Claude Pro", and the current directory path "~\OneDrive\Documents\Agentic PM\vistara_agent". Below the terminal, a chat prompt is visible, starting with "I I need you to publish my Vistara PM Agent project as a polished GitHub repository. Execute all steps. After each step, print a one-line plain-English summary of what you just did so I can follow along in my learning session running in parallel. Details: GitHub username: divyagowdrudinesh Repo name: vistara-pm-agent Visibility: public License: MIT Auth: gh CLI authenticated Source: C:\Users\divya\OneDrive\Documents\Agentic PM\vistara_agent Execute in this order: Step 1 - Staging. Create C:\Users\divya\vistara-pm-agent-repo. Copy all .py files. Do NOT copy .env, .vscode/, __pycache__/, *.pyc. Print: 'Staging directory created with [N] files.'" Step 2 - Secret scan. Grep every .py file for: ATATT,

```
Publish Vistara PM Agent x + v

Step 2 - Secret scan. Grep every .py file for: ATATT,
JIRA_API_TOKEN=, ANTHROPIC_API_KEY=, sk-ant-. If anything
found, STOP and show me. Print: "Secret scan complete -
clean." or list findings.
Step 3 - .gitignore. Create standard Python .gitignore plus:
.env, *.env, venv/, .venv/, __pycache__/, *.pyc, .vscode/,
.idea/, .DS_Store. Print: ".gitignore created."
Step 4 - .env.example. Create with these exact keys,
placeholder values only:
JIRA_API_TOKEN=your_atlassian_api_token_here
JIRA_EMAIL=your_email@example.com
JIRA_BASE_URL=https://your-instance.atlassian.net
ANTHROPIC_API_KEY=your_anthropic_api_key_here
Print: ".env.example created."
Step 5 - requirements.txt. Inspect imports across all .py
files. Include requests, python-dotenv, anthropic with pinned
versions. Print: "requirements.txt created."
Step 6 - Folder structure. Organise files exactly as follows,
then show me the final tree and WAIT for me to type
"confirmed" before proceeding:
vistara-pm-agent/
├── README.md                ← to be written in Step 7
├── LICENSE                  ← MIT
├── .gitignore
├── .env.example
├── requirements.txt
├── agent.py
├── config.py
├── create_epic3.py
├── create_epic4.py
├── create_sprints.py
├── assign_sprints.py
├── add_acceptancecriteria.py
├── fix_storypoints.py
├── fix_subtasks.py
├── fix_subtasks_e3.py
└── backfill_epic1_points.py
```

```
Publish Vistara PM Agent x + v

Step 6 - Folder structure. Organise files exactly as follows,
then show me the final tree and WAIT for me to type
"confirmed" before proceeding:
vistara-pm-agent/
├── README.md                ← to be written in Step 7
├── LICENSE                  ← MIT
├── .gitignore
├── .env.example
├── requirements.txt
├── agent.py
├── config.py
├── create_epic3.py
├── create_epic4.py
├── create_sprints.py
├── assign_sprints.py
├── add_acceptancecriteria.py
├── fix_storypoints.py
├── fix_subtasks.py
├── fix_subtasks_e3.py
├── backfill_epic1_points.py
├── find_sprints.py
├── find_confluence.py
└── debug/
    ├── debug_addcriteria.py
    ├── debug_direct.py
    ├── debug_points.py
    ├── delete_testpage.py
    ├── test_confluence_write.py
    ├── test_personal_direct.py
    └── test_personal_space.py

Step 7 - README.md. Write a complete README with:

Title: vistara-pm-agent
Tagline: "Python agent that builds enterprise-grade Jira +
Confluence portfolios via the Atlassian REST API and
Anthropic Claude API."
Badges: Python 3.10, MIT license
```

```
Publish Vistara PM Agent x + v

Step 7 - README.md. Write a complete README with:

Title: vistara-pm-agent
Tagline: "Python agent that builds enterprise-grade Jira +
Confluence portfolios via the Atlassian REST API and
Anthropic Claude API."
Badges: Python 3.10, MIT license
Why this exists: 4 epics / 42 stories / 9 sprints of real PM
work at Vistara Animation (2022-2025), retrospectively
documented via this agent. Portfolio PDF link placeholder:
[Portfolio - link to be added]
Mermaid architecture diagram
What each script does - one line per script
Quick start: clone → pip install → copy .env.example → fill
in → python agent.py
Key technical decisions: ADF 5-level nesting,
customfield_10037 vs 10016, "Sub-task" hyphenated, Atlassian
404 on expired token
Bug log: all 8 bugs, one line each (root cause + fix)
Author: Divya G D |
https://linkedin.com/in/divya-g-d-824b5b367

Print: "README.md written."
Step 8 - Git init and first commit:
git init
git add .
git commit -m "Initial commit: Vistara PM Jira agent - 4
epics, 42 stories, 9 sprints automated via Atlassian +
Anthropic APIs"
Print: "Git repository initialised and first commit made."
Step 9 - Create remote and push:
gh repo create divyagowdrudinesh/vistara-pm-agent --public
--description "Python agent that builds enterprise-grade Jira
+ Confluence portfolios via the Atlassian REST API and
Anthropic Claude API." --source=. --remote=origin --push
Print: "Repository pushed to GitHub."
Step 10 - Add topics:

Step 8 - Git init and first commit:
git init
git add .
git commit -m "Initial commit: Vistara PM Jira agent - 4
epics, 42 stories, 9 sprints automated via Atlassian +
Anthropic APIs"
Print: "Git repository initialised and first commit made."
Step 9 - Create remote and push:
gh repo create divyagowdrudinesh/vistara-pm-agent --public
--description "Python agent that builds enterprise-grade Jira
+ Confluence portfolios via the Atlassian REST API and
Anthropic Claude API." --source=. --remote=origin --push
Print: "Repository pushed to GitHub."
Step 10 - Add topics:
gh repo edit divyagowdrudinesh/vistara-pm-agent --add-topic
project-management --add-topic jira --add-topic atlassian-api
--add-topic anthropic-claude --add-topic python --add-topic
agentic-ai --add-topic pmo
Print: "Topics added."
Step 11 - Verify and report:

Run git log --all --full-history -- .env → confirm returns
nothing
Print the final repo URL
Print the exact line to paste into my portfolio doc to
replace [TO BE ADDED]
Print any warnings
```

Step-by-Step Execution

Step 1 — Staging Directory

Claude Code created C:\Users\divya\vistara-pm-agent-repo and copied all 20 Python scripts into it — main scripts at root level, debug/test scripts into a debug/ subfolder. The .env file, .vscode folder, and __pycache__ were excluded. It asked for approval before running the file copy command.

```
Publish Vistara PM Agent x + v
DEST="C:/Users/divya/vistara-pm-agent-repo"...
Running...
• Reading 1 file... (ctrl+o to expand)
  $ head -20 "C:/Users/divya/OneDrive/Documents/Agentic PM/vistara_agent/agent.py"

Bash command

SRC="C:/Users/divya/OneDrive/Documents/Agentic PM/vistara_agent"
DEST="C:/Users/divya/vistara-pm-agent-repo"

# Main files
for f in agent.py config.py create_epic3.py create_epic4.py create_epic4.py create_sprints.py assign_sprints.py
add_acceptancecriteria.py fix_storypoints.py fix_subtasks.py fix_subtasks_e3.py backfill_epic1_points.py find_sprints.py
find_confluence.py; do
  cp "$SRC/$f" "$DEST/$f" 2>/dev/null && echo "Copied: $f" || echo "MISSING: $f"
done

# Debug files
for f in debug_addcriteria.py debug_direct.py debug_points.py delete_testpage.py test_confluence_write.py
test_personal_direct.py test_personal_space.py; do
  cp "$SRC/$f" "$DEST/debug/$f" 2>/dev/null && echo "Copied: debug/$f" || echo "MISSING: debug/$f"
done

echo "---"
find "$DEST" -name "*.py" | wc -l
Copy all Python files to staging directory with correct folder structure

Unhandled node type: string

Do you want to proceed?
> 1. Yes
   2. No

Esc to cancel · Tab to amend · ctrl+e to explain
```

Claude Code showing the bash command before execution — source/destination variables, copy loops for main and debug files, and file count verification. Permission requested before any file system operation.

Step 2 — Secret Scan

Claude Code scanned every .py file for hardcoded secrets (ATATT, JIRA_API_TOKEN=, ANTHROPIC_API_KEY=, sk-ant-). Result: No matches found. All scripts use os.getenv() to read credentials from the .env file at runtime — never hardcoded. Safe to proceed.

Steps 3, 4, 5 — Support Files

Three files were written in parallel: .gitignore (49 lines covering Python, virtual environments, IDE folders, macOS/Windows system files), .env.example (4 lines with placeholder values for all required credentials), and requirements.txt (requests==2.31.0, python-dotenv==1.0.0, anthropic==0.25.0).

Step 6 — Folder Structure (Confirmation Gate)

Claude Code displayed the complete folder tree and paused — waiting for explicit 'confirmed' before proceeding. This was the safety gate built into the prompt to prevent Claude Code from autonomously proceeding to git operations without review.

```
Publish Vistara PM Agent x + v

Listed 1 directory (ctrl+o to expand)

Here is the final folder structure for your review (Step 6 - please type "confirmed" to proceed):

vistara-pm-agent-repo/
├── README.md
├── LICENSE
├── .gitignore
├── .env.example
├── requirements.txt
├── agent.py
├── config.py
├── create_epic3.py
├── create_epic4.py
├── create_sprints.py
├── assign_sprints.py
├── add_acceptancecriteria.py
├── fix_storypoints.py
├── fix_subtasks.py
├── fix_subtasks_e3.py
├── backfill_epic1_points.py
├── find_sprints.py
├── find_confluence.py
├── debug/
│   ├── debug_addcriteria.py
│   ├── debug_direct.py
│   ├── debug_points.py
│   ├── delete_testpage.py
│   ├── test_confluence_write.py
│   ├── test_personal_direct.py
│   └── test_personal_space.py
└──

20 Python files staged. No secrets found. .gitignore, .env.example, requirements.txt, LICENSE, and README.md all written.

---
Steps completed so far:
```

```
Publish Vistara PM Agent x + v

├── find_sprints.py
├── find_confluence.py
├── debug/
│   ├── debug_addcriteria.py
│   ├── debug_direct.py
│   ├── debug_points.py
│   ├── delete_testpage.py
│   ├── test_confluence_write.py
│   ├── test_personal_direct.py
│   └── test_personal_space.py
└──

20 Python files staged. No secrets found. .gitignore, .env.example, requirements.txt, LICENSE, and README.md all written.

---
Steps completed so far:
- Step 1 - Staging directory created with 20 files.
- Step 2 - Secret scan complete - clean.
- Step 3 - .gitignore created.
- Step 4 - .env.example created.
- Step 5 - requirements.txt created (requests==2.31.0, python-dotenv==1.0.0, anthropic==0.25.0).
- Step 6 - Folder structure ready - waiting for your "confirmed".
- Step 7 - README.md written.

One note I'll flag at Step 11: debug/debug_direct.py contains a hardcoded email address (divyagowdrudinesh@gmail.com). The token is already a placeholder (PASTE_YOUR_TOKEN_HERE), so no secret is exposed, but be aware the email will be public. Type "confirmed" to proceed to git init and push.

*Cooked for 3m 16s

*recap: Publishing your Vistara PM Agent project to GitHub. All files are staged and verified - waiting for you to type "confirmed" to proceed with git init, first commit, and push. (disable recaps in /config)

> |

>> accept edits on (shift+tab to cycle) X Auto-update failed · Try claude doctor or npm i -g @anthropic-ai/claude-code
```

Step 6 confirmation gate: complete folder tree displayed — 20 Python files, debug/ subfolder with 7 scripts, README.md, LICENSE, .gitignore, .env.example, requirements.txt. Status summary at bottom confirms all steps 1–7 complete. 'confirmed' typed to proceed.

Step 7 — README.md

Claude Code read the actual source scripts before writing the README — it called head on create_epic3.py and debug_addcriteria.py to understand the real code structure. The README was written from code evidence, not assumption. 129 lines written covering: title, badges, why this exists table, Mermaid architecture diagram, script-by-script table, quick start, key technical decisions, and bug log.

Steps 8, 9, 10 — Git Init, Push, Topics

git init initialized a local repository. git add . staged all files. The first commit message was: 'Initial commit: Vistara PM Jira agent — 4 epics, 42 stories, 9 sprints automated via Atlassian + Anthropic APIs'. gh repo create pushed directly to GitHub as a public repository with the correct description. gh repo edit added 7 topics: python, jira, project-management, pmo, atlassian-api, anthropic-claude, agentic-ai.

Step 11 — Verification

git log --all --full-history -- .env returned nothing — confirming the .env file was never committed. The .gitignore successfully excluded it from the entire git history, not just the working directory.

Post-Push: Hallucination Corrections

After the repository went live, two inaccuracies were identified in the README and corrected via a follow-up Claude Code session. This is documented here because it demonstrates structured QA discipline — catch, diagnose, fix, verify — rather than accepting automated output without review.

Error Found	Correction Made
Sub-tasks count showed '20+' in the Why this exists table	Corrected to '9' — the actual number of subtasks across all 4 epics
Bug log listed 8 different bugs derived from code inference rather than the documented bugs in the portfolio	Rewrote bug log to match the 8 bugs documented in Section 7 of this portfolio — same root causes, same fixes, consistent narrative across both documents

Both corrections were committed as a second commit to the repository, keeping the git history transparent.

Final Repository — Verified State

divyagowdrudinesh / vistara-pm-agent

Type / to search

<> Code

Issues

Pull requests

Actions

Projects

Wiki

Security and quality

Insights

Settings

vistara-pm-agent

Public

Pin

Watch 0

Fork 0

Star 0

master

1 Branch

0 Tags

Go to file

Add file

<> Code

divyagowdrudinesh-hub

Initial commit: Vistara PM Jira agent — 4 epics, 42 stories, 9 sprint...

7fe7f1a · 10 minutes ago

1 Commit

debug	Initial commit: Vistara PM Jira agent — 4 epics, 42 stories, 9 ...	10 minutes ago
.env.example	Initial commit: Vistara PM Jira agent — 4 epics, 42 stories, 9 ...	10 minutes ago
.gitignore	Initial commit: Vistara PM Jira agent — 4 epics, 42 stories, 9 ...	10 minutes ago
LICENSE	Initial commit: Vistara PM Jira agent — 4 epics, 42 stories, 9 ...	10 minutes ago
README.md	Initial commit: Vistara PM Jira agent — 4 epics, 42 stories, 9 ...	10 minutes ago
add_acceptancecriteria.py	Initial commit: Vistara PM Jira agent — 4 epics, 42 stories, 9 ...	10 minutes ago
agent.py	Initial commit: Vistara PM Jira agent — 4 epics, 42 stories, 9 ...	10 minutes ago
assign_sprints.py	Initial commit: Vistara PM Jira agent — 4 epics, 42 stories, 9 ...	10 minutes ago
backfill_epic1_points.py	Initial commit: Vistara PM Jira agent — 4 epics, 42 stories, 9 ...	10 minutes ago
config.py	Initial commit: Vistara PM Jira agent — 4 epics, 42 stories, 9 ...	10 minutes ago
create_epic3.py	Initial commit: Vistara PM Jira agent — 4 epics, 42 stories, 9 ...	10 minutes ago
create_epic4.py	Initial commit: Vistara PM Jira agent — 4 epics, 42 stories, 9 ...	10 minutes ago
create_sprints.py	Initial commit: Vistara PM Jira agent — 4 epics, 42 stories, 9 ...	10 minutes ago

About

Python agent that builds enterprise-grade Jira + Confluence portfolios via the Atlassian REST API and Anthropic Claude API.

python

jira

project-management

pmo

atlassian-api

anthropic-claude

agentic-ai

Readme

MIT license

Activity

0 stars

0 watching

0 forks

Releases


No releases published

Create a new release


Packages

No packages published

Live GitHub repository — github.com/divyagowdrudinesh/vistara-pm-agent. All files present: debug/ folder, .env.example, .gitignore, LICENSE (MIT), README.md, 13 core scripts, requirements.txt. Topics visible in sidebar: python, jira, project-management, pmo, atlassian-api, anthropic-claude, agentic-ai. Languages: Python 100%.

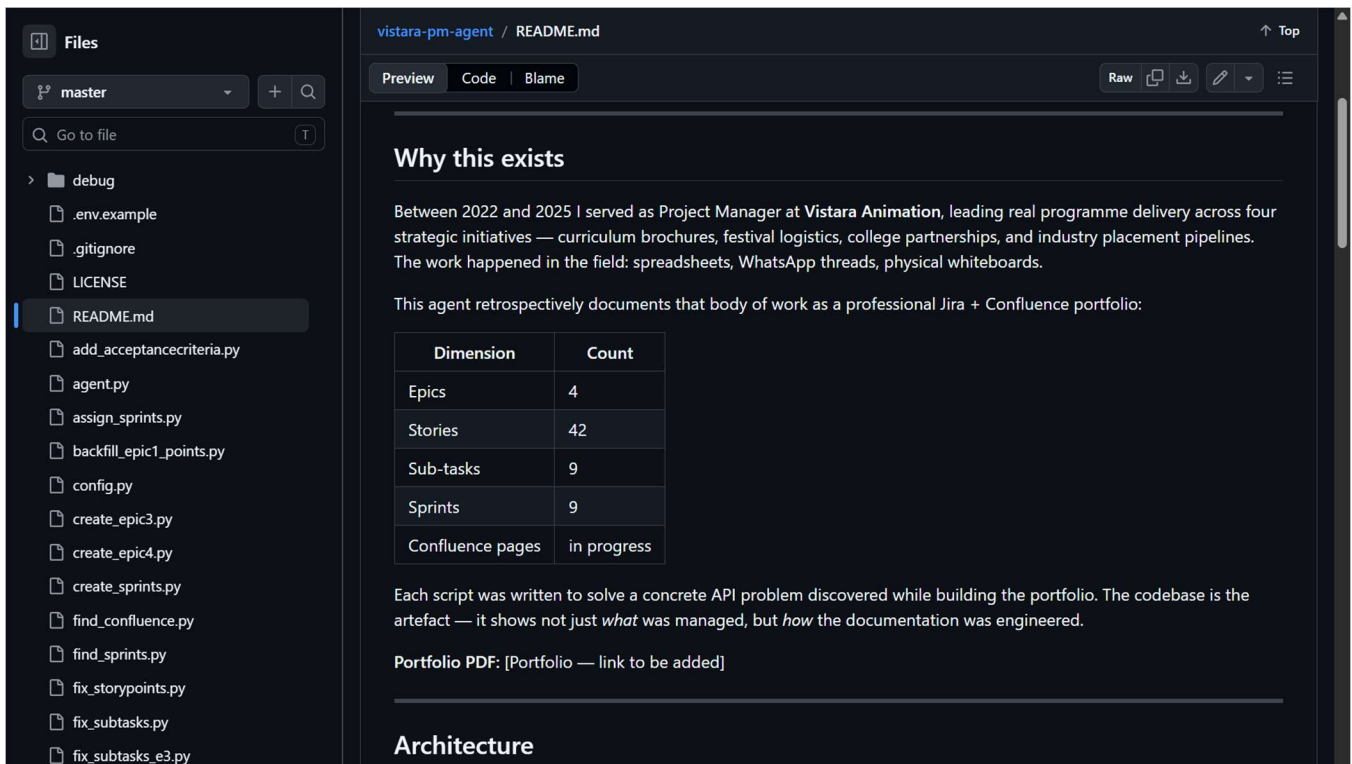

README — Why this exists section: correct table showing 4 epics, 42 stories, 9 sub-tasks, 9 sprints. Architecture section visible below.

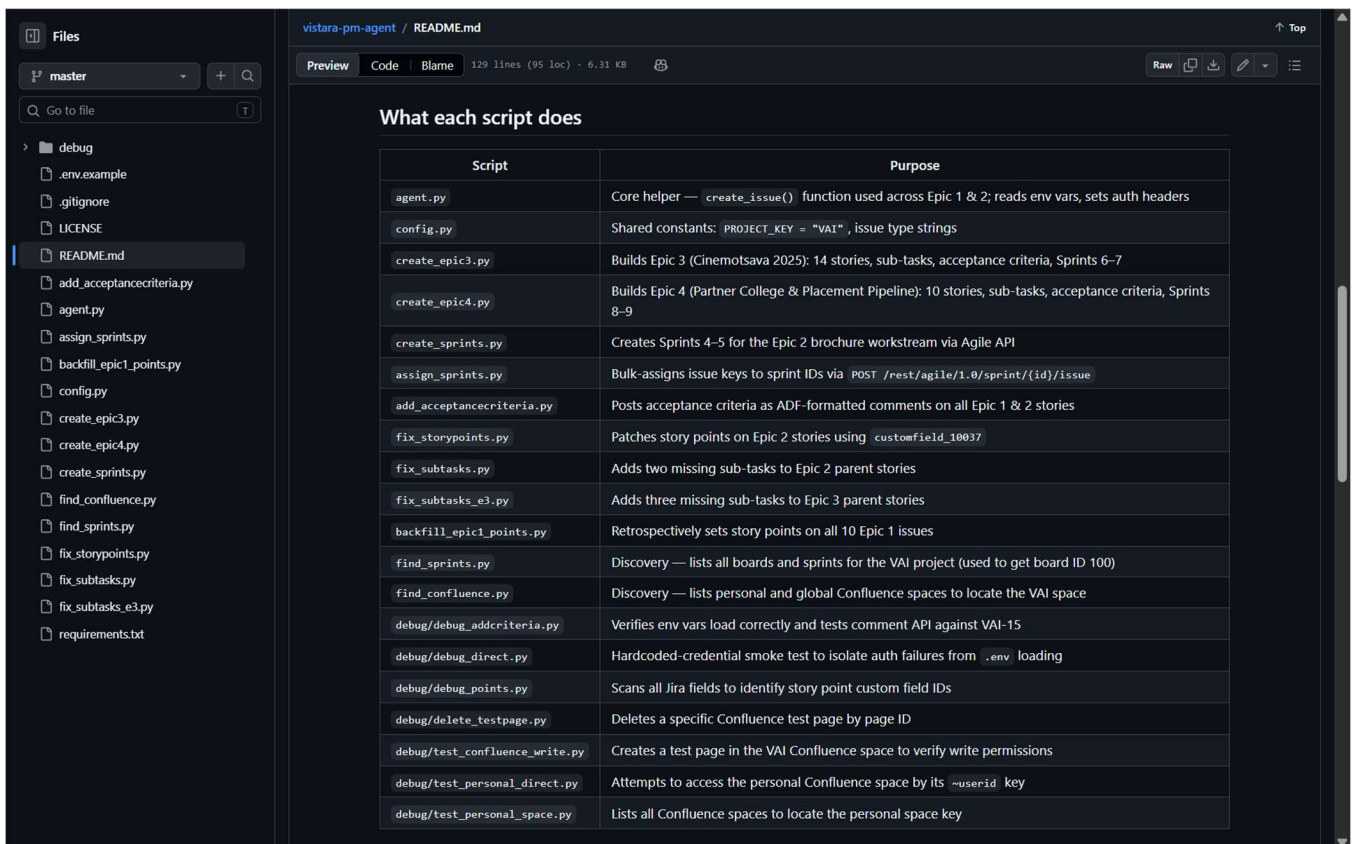

README — What each script does table: all 20 scripts documented with accurate one-line descriptions derived from actual code reading, not assumptions.

Files

master

Go to file

debug

- .env.example
- .gitignore
- LICENSE
- README.md
- add_acceptancecriteria.py
- agent.py
- assign_sprints.py
- backfill_epic1_points.py
- config.py
- create_epic3.py
- create_epic4.py
- create_sprints.py
- find_confluence.py
- find_sprints.py
- fix_storypoints.py
- fix_subtasks.py
- fix_subtasks_e3.py
- requirements.txt

vistara-pm-agent / README.md

Preview Code Blame 129 lines (95 loc) · 6.31 KB

Raw Copy Download Edit

Quick start

```
# 1. Clone
git clone https://github.com/divyagowdrudinesh/vistara-pm-agent.git
cd vistara-pm-agent

# 2. Install dependencies
pip install -r requirements.txt

# 3. Configure credentials
cp .env.example .env
# Open .env and fill in your Atlassian API token, email, base URL, and Anthropic key

# 4. Run the main agent
python agent.py
```

Key technical decisions

1 — customfield_10037 not customfield_10016

Jira Cloud uses two different custom field IDs for story points depending on whether the project uses next-gen or classic boards. `customfield_10016` is the next-gen field; `customfield_10037` is the classic Software board field. `debug_points.py` was written specifically to enumerate all field IDs and find the correct one.

2 — "Sub-task" (hyphenated)

The Jira REST API v3 rejects `"Subtask"` with a 400. The correct issue type name is `"Sub-task"` with a hyphen. This is not documented prominently in the official docs.


3 — Atlassian 404 on expired token

When an Atlassian API token expires, the platform returns 404 (not 401). This means expiry looks like a missing resource, not an authentication failure. Always check token validity first when you see unexpected 404s on known issue keys.


4 — ADF 5-level nesting for acceptance criteria

Confluence Atlassian Document Format requires a strict content hierarchy for structured content: `doc` → `bulletList` → `listItem` → `paragraph` → `text`. Flattening or skipping any level causes a 400 with a cryptic schema validation error.

README — Quick start section showing exact clone URL, pip install, .env setup, and run command. Key technical decisions section below covering customfield_10037 vs 10016 and Sub-task hyphenation.

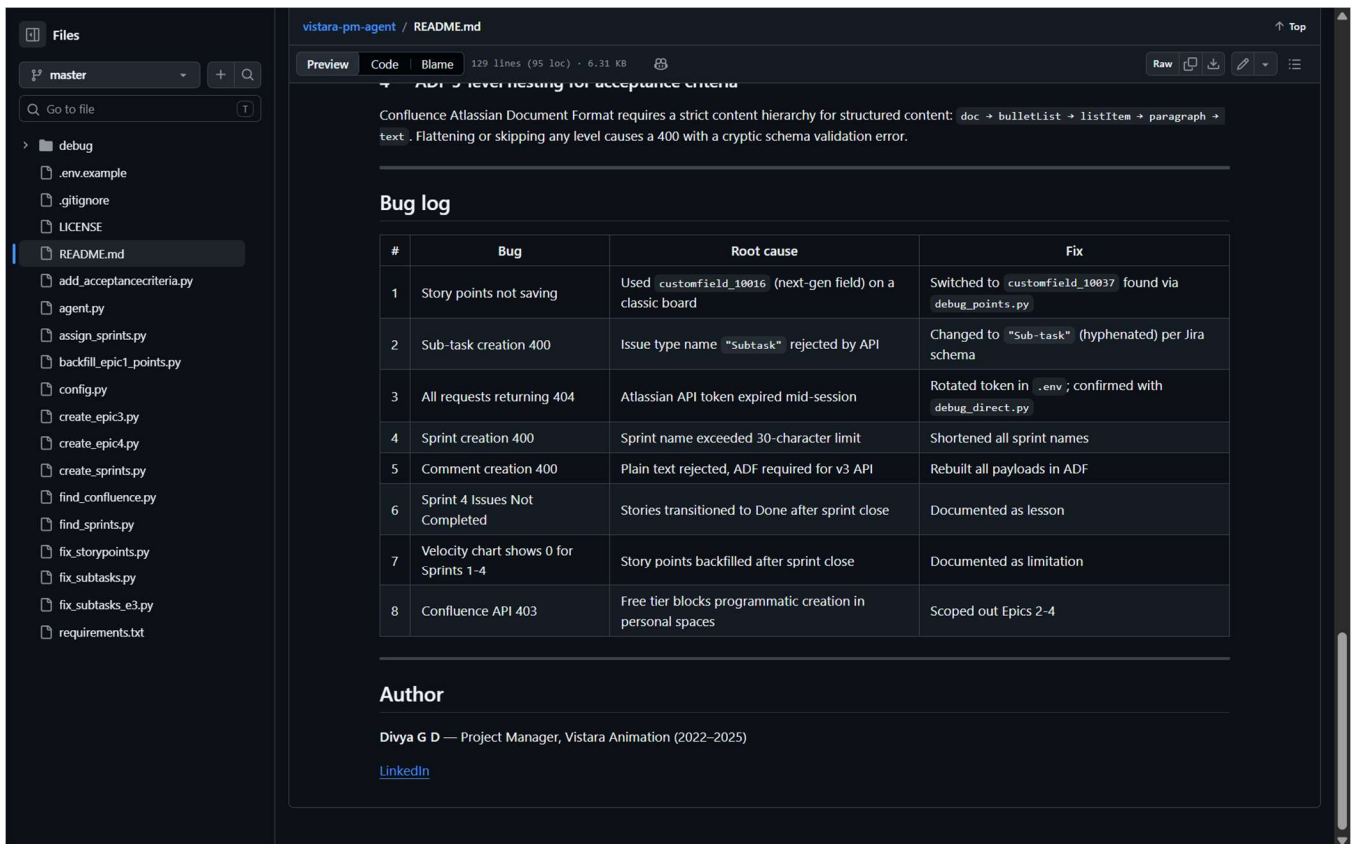

README — Corrected bug log (post-QA): all 8 bugs aligned with portfolio Section 7. Bugs 1–8 documented with root cause and fix. Author section below with LinkedIn link.

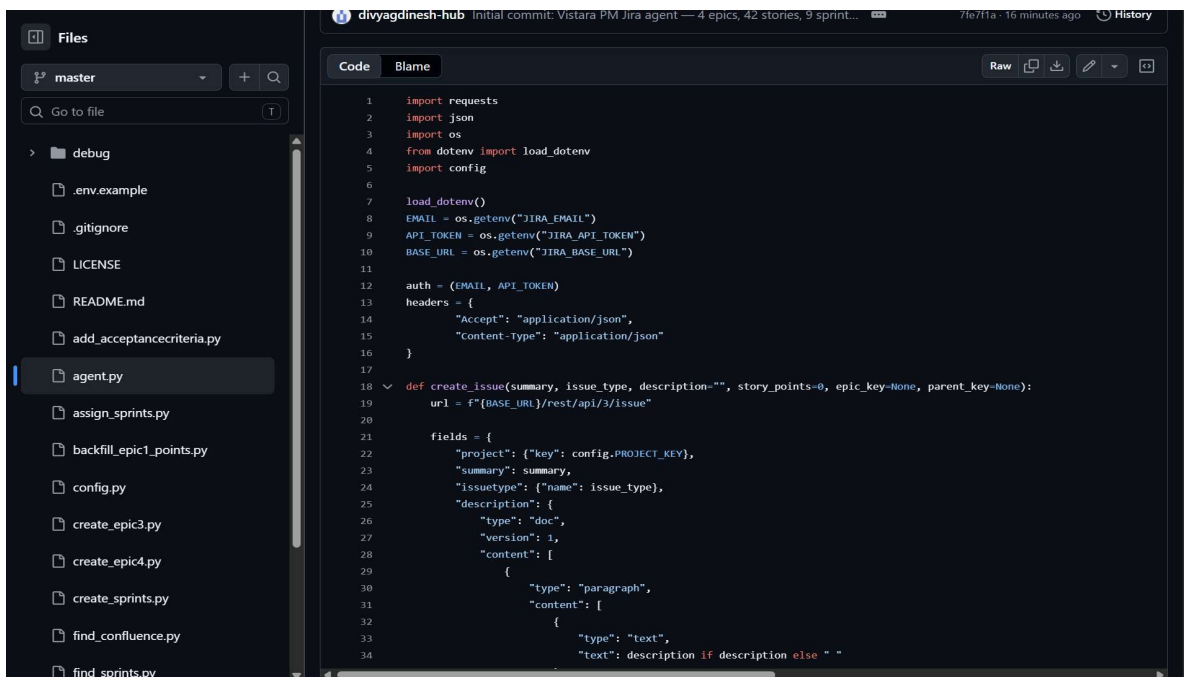

agent.py viewed in GitHub: lines 1–34 showing clean credential handling — `os.getenv()` reads `EMAIL`, `API_TOKEN`, `BASE_URL` from `.env` at runtime. No hardcoded values. ADF description structure visible from line 25.

What This Section Demonstrates

Publishing a technical project to GitHub is itself a PM competency in 2026. It required: toolchain evaluation (Node.js, Git Bash, Claude Code), security discipline (.env exclusion, secret scan), structured prompt design (11-step execution sequence with explicit confirmation gates), QA after automated output (hallucination identification and correction), and version control hygiene (clean commit history, .gitignore coverage).

The repository is publicly accessible and serves as the live, browsable version of this portfolio document. All scripts are readable, the README is self-contained, and the commit history shows the build and QA process transparently.

Section 10: Links & Access

Artefact	Location / Access
Jira Portfolio Board	Jira Portfolio - Overview (available on request)
Confluence Documentation	Confluence Pages (available on request)
GitHub Repository	https://github.com/divyagowdrudinesh/vistara-pm-agent
LinkedIn Profile	linkedin.com/in/divya-g-d-824b5b367
Growth School PM Cert	Credential ID: a3a77b22-9c62-4296-b2a9-fe0c45d7777a
Vistara OPC Registration	CIN: U85500KA2024OPC188895 — verifiable via MCA portal
BIET MoU	Ref. BIET/SR/Office/G28/24-25, dated Jun 25, 2024 — available on request

Note: Jira and Confluence are on a free-tier Atlassian account. If access is needed for interview review, please request via email and a read-only viewer link will be shared.

Contact: divyagowdrudinesh@gmail.com · +91 9945607229
